

COMMUNITY COLLEGE DISTRICT

Measure A/B Bond Program

Citizens' Bond
Oversight Committee
Report

October 23, 2019



### Chabot-Las Positas Community College District Measure B & A Citizens' Oversight Committee 2020 Fifteenth Annual Report to the Community Proposed Timeline

**November 01 or Earlier**- Begin writing, getting content and getting photos

**November 07** – First Draft Report to Designer

**November 11** – Veterans' Day – CLPCCD Holiday

**November 16** – Team to meet with Designer to review first draft

**November 20** – Final Comments to Designer

November 27 through November 29 – CLPCCD Holiday

**December 05** - Proof back from Designer - copies to District Office to proof

**December 12**– Email the draft report to COC Chair and Committee for their review only

**December 17** – Confirmation receipt from COC Chair and Committee via: email

**December 19** - The final report send to Printer

**December 24 through January 01** – CLPCCD Holiday

**January 09** – 300 copies delivered to CLPCCD from Printer

**January 10** – Chancellor's office will mail copies to BOT members

**January 20** – Martin Luther King Day – CLPCCD Holiday

**January 21 -** Presentation to and acceptance by Board of Trustees (Date: Coordinate with the Chancellor's Office)

**January 24 - Pending** - Distribution through Bay Area News Group (Pending 01/27/2020 Subscribers and 01/28/2020 non-subscribers)

### Citizens' Oversight Committee

### 2020 Meeting Calendar

S	M	T	W	T	F	S			
	JANUARY								
	1	2	3	4	5	6			
7	8	9	10	11	12	13			
14	15	16	17	18	19	20			
21	22	23	24	25	26	27			
28	29	30	31						
	( P								

6 PM - District Offi	0	PM -	District	Offic
----------------------	---	------	----------	-------

M	T	W	T	F	S
	FEB	RU	ARY		
					1
3	4	5	6	7	8
10	11	12	13	14	15
17	18	19	20	21	22
24	25	26	27	28	29
	3 10 17	FEB  3 4  10 11  17 18	FEBRUA  3 4 5  10 11 12  17 18 19	FEBRUARY  3 4 5 6  10 11 12 13  17 18 19 20	FEBRUARY  3 4 5 6 7  10 11 12 13 14  17 18 19 20 21

S	M	T	W	T	F	S
		M	ARC	СН		
					1	2
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				
			•			

S	M	T	W	T	F	S
		A	PRI	L		
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30		

6 PM -Chabot College

S	M	T	W	T	F	S
		]	MAY	7		
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

- 8	M	1	W	1	r	8
		J	UNI	$\Xi$		
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				
_			-			

S	M	T	W	T	F	S		
JULY								
			1	2	3	4		
5	6	7	8	9	10	11		
12	13	14	15	16	17	18		
19	20	21	22	23	24	25		
26	27	28	29	30	31			
(	6 PM	- Las	S Posi	tas C	olleg	e		

6 PM - Las Positas College	6	PM -	Las	<b>Positas</b>	College
----------------------------	---	------	-----	----------------	---------

S	M	T	W	T	F	S
		Αl	JGU	ST		
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

		SEP	ГЕМ	BER	2	
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

S	M	1	W	1	F	S
		OC	TOE	BER		
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

6 PM - District Office

S	M	T	W	T	F	S
NOVEMBER						
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

S	M	T	W	T	F	S
DECEMBER						
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

Citizens' Bond Oversight Committee Report Chabot-Las Positas Community College District July to September 2019

#### Las Positas College

All Measure B related projects are completed and closed at this time.

As of September 30, 2019, LPC has spent and committed \$248M or 99% of the campus Measure B program budget.

#### <u>Chabot College – Biology Building</u>

The new Biology Building at Chabot College, received DSA approval in November 2017. The program for the new building includes five new teaching laboratories with adjacent prep rooms, a Cadaver room, greenhouse and teaching support spaces. It will be located in what is now parking lot C, adjacent to the existing Biology Building 2100.

The Board approved the Construction contract in February 2018 and construction commenced on March 12, 2018 with substantial completion in Winter 2020. As of December 31, 2018, Chabot College has spent and committed \$259 million, or 98% of their total Measure B budget allocation.

Construction began March 2018. Metal stud framing and Mechanical, Electrical, Plumbing, work in progress. Anticipated completion is March 2020. First classes expected Summer 2020.

#### California Energy Commission Grant

The District was awarded a \$1.5M EPIC demonstration grant from the California Energy Commission to plan, design and install a Microgrid on the Las Positas campus incorporating a new 1 Megawatt-hour flow battery coupled with the college's 2.3MW solar PV array and ice storage units to better utilize the energy generated on site and purchased from PG&E. Measure B is providing \$500,000 in local matching funds to leverage this state grant.

Final PG&E approval to operate was finalized in August 2018 after final system testing. The battery systems are preforming and the new Demand Charge Management Application is operational. Simple payback on the District's investment is expected to be five years. The final report to the Energy Commission was submitted and below is a link to the final Energy Commission Report.

https://ww2.energy.ca.gov/2019publications/CEC-500-2019-052/CEC-500-2019-052.pdf.

#### Measure A

The Measure A funding has provided the District the opportunity to upgrade technology throughout both campuses and bring connectivity to every corner of the campuses in the first year of the program. Moving forward we have envisioned new and renovated facilities at the Chabot College campus to improve our facilities and address student needs across all disciplines. Las Positas College will see growth of existing programs and expansion of the campus to provide better access to facilities to all students including veterans, those with disabilities, and pursuit of career pathways. Each campus will begin the program with construction of student support space and expansion of learning resource facilities to align with the Districts "Vision for Success".

#### <u>Las Positas College – New Academic Support and Office Building 2100</u>

The new Academic Support and Office building will be built in the location of existing buildings 2100 & 2200. The project will consist of the following elements and programs: English Center incorporating classrooms, computer lab, tutoring and study areas. Math Center incorporating classrooms, labs and the Math X program. Computer Sciences Center including computer labs, networking, maker space and open labs with the expanded of library functions including reference desk, study areas, computer lab, expanded staff offices and library operational support spaces. Faculty Offices for 80 faculty and 25 adjunct faculty, dean's suite and support spaces will also be located in the building.

The Project kick-off meeting took place in early March 2019. Programming of the building completed June 2019 with the Schematic Design Phase was completed in early September 2019. Design Development phase has kicked off with Use Group and technical meetings taking place in early October 2019. Meetings with DSA and Livermore Fire have occurred in late August/September 2019.

### <u>Las Positas College – Public Safety Center/Advanced Manufacturing and Transportation</u> Facilities (PSC/AMT)

The new Public Safety Center/Advanced Manufacturing and Transportation Facilities (PSC/AMT) will replace outdated facilities in Buildings 600A, 800 and 2200. The Public Safety programs that will be located in the New Building include, the Administration of Justice, Fire Service Technology and Emergency Medical Services programs. A Risk Management Tower, is planned as part of the Fire Service Technology program. The Advanced Manufacturing and Transportation programs will be located in the New Building will include Auto Technology, Advanced Manufacturing and the Welding Technology programs. There will be shared support spaces for both programs that include, classrooms, computer labs, collaborative spaces, faculty offices, etc.; The expansion of Parking Lot O adding up to 200 new spaces.

The Project Kick-off meeting took place June 5, 2019. Programming of the building completed in August 2019. Schematic Design phase is nearly complete. With the Design Development Phase anticipated to start in November 2019 with additional User Group and technical meetings with design team and their sub-consultants.

#### <u>Las Positas College – New Horticulture Facility</u>

The New Horticulture Facility will replace the facilities currently located in Building 800 and located outdoors and be located near the Maintenance and Operations facility and the Track and Field at the upper NE part of campus. The project includes, additional parking for a 75 space parking lot for faculty and students. The Horticulture Facility includes classrooms, Labs, offices and resource area, a greenhouse, shade structures. The outdoor growing areas will have soil bins, equipment storage and an outdoor learning patio.

The Project Kick-off meeting will be set for early August 2019. The Programming Phase of the building and outdoors spaces will complete mid-October 2019. Schematic Design/Design Development Phase will begin in late October 2019, with the continuation of User Group meetings.

#### Las Positas College - New Viticulture Facility

The New Viticulture Facility will replace the existing facilities currently located in/outside of Building 800. The Viticulture Facility will be located at the main entrance off the Campus Hill Road. This new roadway will connect the new facilities into the existing campus. The new facility will be developed at a higher elevation allowing for expansive views. The project will be including general site grading and utility infrastructure; New Roadway and Pedestrian pathways connecting to the existing campus. A Visitor Center with Tasting room, visitor Parking and clear paths of travel, A Winemaking Facility including classrooms and Labs, office and resource areas, Crush pad, Equipment storage, cold storage, and an Outdoor Patio.

Design Proposals were received in August 2019. Interviews were held on August 23, 2019. The committee recommended to award Design Services to tBP/Architecture. The Board approved the contract at the September 2019 Board Meeting. The Project Kick-off meeting for infrastructure portion of the project is scheduled to happen in late October 2019.

### <u>Las Positas College – Temporary Office Complex: Faculty Office Relocation Facility</u>

The project includes providing modular buildings to accommodate ~ 75 faculty offices, conference rooms, and support spaces. In addition, a modular restroom unit will be provided to support the occupants. A raised, covered walkway with ramps will be provided to connect the modular buildings and modular restroom unit.

Design Services for LPAS was approved at the October 2019 Board Meeting. Anticipation of the Project Kick-off meeting to happen in early November 2019.

#### <u>Las Positas College – Soccer Field Replacement Project</u>

The existing synthetic turf soccer field at Las Positas College is approximately 11+ years old. The project will remove and dispose of the existing synthetic turf, removal and disposal of the existing shock/drain pad beneath the turf and correct, as needed, the existing permeable base. Install new shock/drain pad, and complete the installation of the new turf product, including permanent NCAA/FIFA lines and marking for soccer and school logo. New removable bollards and protective netting will be installed for safety measures.

Demolition of the existing field is complete. Grading for new turf is completed. Currently installing fabric, pad and turf. Upcoming is install of infill, bollards and netting, followed by clean-up and punch list.

#### Las Positas College – B2400 AV Wall Upgrade Room 2420

The existing audio-visual system in room B2420 is comprised of three projectors and a screen which includes AV controls at the lectern. The existing system will be replaced with LED flat panel system, movable lectern, upgraded speakers and cameras.

Design and DSA permitting completed, Pre-Bid Conferences were completed, Bidding is currently under review. Potential Board Approval in November 2019, with Construction to happen during the Winter Break.

#### Chabot College – Fire Alarm Voice Evacuation Project

Campus-wide Fire Alarm Voice Evacuation Project will Replace existing horn/strobe system throughout the Chabot College campus with a new evacuation speaker/strobe system. The existing fire alarm control panels will remain and have additional components added for the evacuation system. The project was DSA approved in September 2018; contract was awarded in December 2018 and construction started in January 2019.

Construction started January 2019. Pacific Power & Systems are working on network and device height issues. Device installation to begin October 2019.

#### New Baseball Field Project

The Baseball Field Project will be the colleges first Design-Build project. The project consists of the removal and replacement of existing baseball field. This project will replace and improve infrastructure and drainage systems, lighting, press box, dugouts, bleachers,

scoreboard, fencing and backstops. Renovation of ADA compliant restrooms, and provide accessible compliant paths of travel. Board approved Robert A. Bothman Construction for Design-Build contract.

Project entered into pre-construction services to develop Guaranteed Maximum Price (GMP). GMP for Design/Construction phase contract approved at the September 17, 2019 BOT meeting. Construction documents are being prepared. Anticipated DSA submittal is November 2019. Construction phase expected to be May 2020 – February 2021.

#### MPOE – Renovation and Relocation of B300 Project

This project renovates a major portion of the first floor of Building 300 to serve the current and future capacity for telephone and internet connectivity and to provide new space for new Distributed Antenna Systems (DAS) for cell phone signal improvement at the campus.

ATI architects + Engineers submitted project to DSA in August 2019. Awaiting plan check comments. Construction is anticipated to begin June 2020.

#### Pool Renovation Project


This project will demolish and install new pool plaster, replace pool handrails, ceramic tile and hardware, repair surrounding pool deck and install new perimeter fence.

Design contract awarded to Arch-Pac Aquatics on July 16, 2019 board meeting. Arch-Pac Aquatics completed the construction documents. Construction project awarded to Western Water Features, Inc. October 15, 2019 at the BOT meeting. Construction to be October 2019 – December 2019.

### District-Wide Campus Security Exterior Lighting

This project will install additional lighting poles along with the replacement of existing light poles and wall packs with brighter LED fixtures at the exterior of multiple buildings and multiple outside locations at both Chabot and Las Positas College.

Project received bids September 2019 and post interviews were conducted. Project expected to be awarded to lowest bidder at the BOT meeting October 2019.



C H A B O T - L A S P O S I T A S | Community College District

### Hayward Fire Training Center

Joint Use Facility and Ground Lease Update **Sept 2019** 



- City of Hayward
  - \$73 Million investment
  - Replace Fire Station #6
  - Construct New Fire Training Center
  - Located at Hayward Executive Airport
    - 1401 West Winton Avenue






- City of Hayward
  - \$53 Million investment
- Hayward Executive Airport
  - Ground Lease
- Chabot College
  - \$20 Million investment (Measure A)





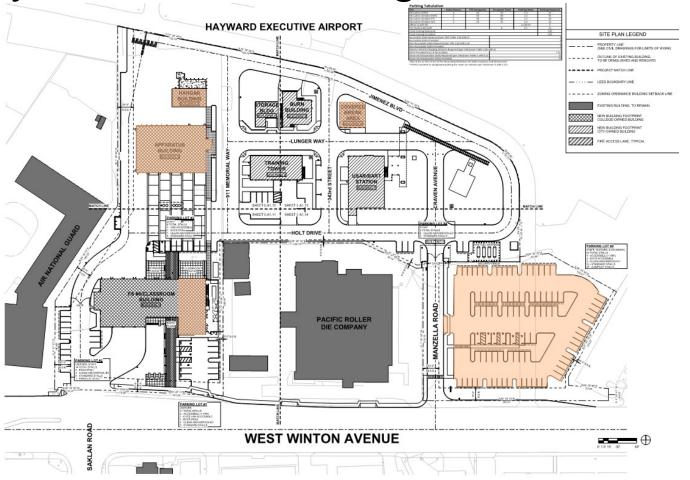















































### Next Steps

- Division of the State Architect (DSA) approval
- City of Hayward Building Permit
- Prequalification of Contractors (City)
- Bidding (City)
- Ground Breaking Ceremony
- Construction Period (18 to 24 months)
- Ribbon Cutting Ceremony





Facilities Modernization Program Measure B & A - Project Report

October 23, 2019





### **Project Team:**

Architect: Harley Ellis Devereaux

**Construction Manager**: Vanir Construction Management

Contractor: W. A. Thomas Construction, Inc.

### **Project Update:**

- Preparing framing for Curtain wall & Storefront Glazing
- Installing roof top ductwork at the mechanical shaft
- Installing exterior framing at roof terrace

Occupancy: Spring/Summer 2020



# PROJECT PROGRESS REPORT Fire Alarm System Voice Evacuation Upgrade – Measure A

CHABOT COLLEGE October 23, 2019





### **Project Team:**

**Architect**: WKM Electrical Consultants Inc.

**Construction Manager**: Swinerton Management & Consulting

Contractor: Pacific Power & Systems Inc.

### **Project Description:**

The project consist of the campus-wide removal and replacement of the existing horn/strobe fire alarm system with a new evacuation speaker/strobe system.

### **Project Update:**

- •Currently troubleshooting network issues.
- •Device installation expected to start in September

Occupancy: Winter 2019

### PROJECT PROGRESS REPORT

### **Building 100 New Library and Learning Connection Project – Measure A**

October 23, 2019





### **Project Team:**

**Architect**: Group 4 Architects

**Construction Manager**: Swinerton Management & Consulting

Contractor: TBD

### **Project Description:**

Project consists of construction of a new Library and Learning Connection building in the grand court of the Chabot campus. New building to contain, but is not limited to, space for Library functions, ESL, WRAC, Learning Connection Center, and collaborative spaces

### **Project Update:**


- Schematic Design Phase in progress
- •Recently met with Hayward fire in order to plan fire access around new building
- •User Group meetings being held to finalize adjacency and show rough ideas for general building design

Occupancy: TBD

# PROJECT PROGRESS REPORT District-Wide Campus Security Exterior Lighting

### October 23, 2019



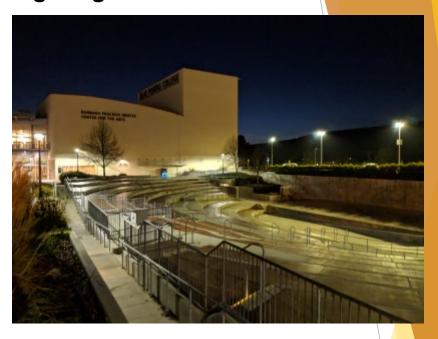

### **Project Team:**

**Architect**: WKM Electrical Consultants Inc.

Construction Manager: Swinerton Management & Consulting

**Contractor**: Nema Construction (Apparent Low Bidder)

### **Project Description:**

Installation of additional lighting poles along with the replacement of existing light poles and wall packs with brighter LED fixtures at the exterior of multiple buildings and multiple outside locations at both Chabot and Las Positas College.

### **Project Update:**

- Bids received on September 24<sup>th</sup> ,2019. Low bid by Nema construction totaling \$522k
- Post bid interview conducted
- Awaiting October 15 board meeting, NOIA to be sent to Nema Construction

# PROJECT PROGRESS REPORT Athletic Field Improvement Project – Measure A

October 23, 2019



**Project Team:** 

Bridging Architect: HMC Architects (Design-Build)

**Construction Manager**: CCM/STV Joint Venture

**Design Build Entity**: Robert A Bothman Construction

**BCA Architects** 

### **Project Description:**

Project consists of the removal and replacement of the existing baseball field with artificial turf. Install new bleachers, site lighting, dugouts, batting cages, bullpens, storage areas, and scoreboard along with the new code-compliant press box structure with restrooms and accessible pathways.


### **Project Update:**

- Board awarded the construction contract at Sept 17 meeting
- Kick-off meeting held on Oct 3
- 4th Quarter 2019 Finalize Construction Documents

Occupancy: February 2021

# PROJECT PROGRESS REPORT MPOE Renovation & Relocation Project – Measure A

October 23, 2019

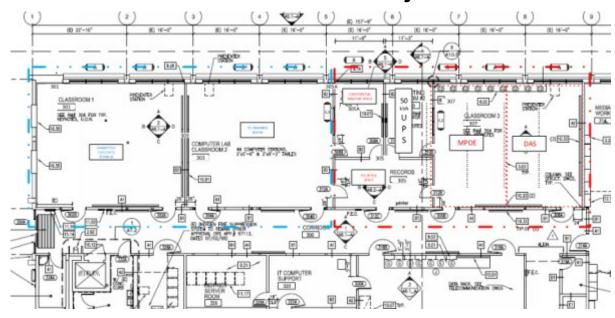

**Project Team:** 

**Architect**: ATI Architect + Engineers

Construction Manager: CCM/STV Joint Venture

**Contractor**: TBD

### **Project Description:**

This project renovates a major portion of the first floor of Building 300 to serve the current and future capacity for telephone and internet connectivity and to provide new space for new Distributed Antenna Systems (DAS) equipment for cell phone signal improvement at the campus.

### **Project Update:**

- Design documents at DSA for review and comment
- Site meeting with the Director of DSPS on Sept 30 for potential relocation spaces
- Documents submitted for review at Alameda County Dept. of Health on Oct 1

Occupancy: October 2020

# PROJECT PROGRESS REPORT Pool Renovation Project

October 23, 2019



**Project Team:** 

Architect: Arch-Pac

**Construction Manager**: CCM/STV Joint Venture

Contractor: TBD

### **Project Description:**

This project will demolish and install new pool plaster, repair surrounding pool deck, install new perimeter fence and replace pool handrails, ceramic tile, and hardware.

### **Project Update:**

- Bid opening September 30th, 2019
- Two bids received; lowest bidder was Western Water Features, Inc. at \$889,000.00
- NOIA issued Oct 3

Occupancy: January 2020



Facilities Modernization Program
Funded by Measure A/B
Project Report

October 23, 2019

### PROJECT PROGRESS REPORT New Academic Support and Office Building 2100

# LAS POSITAS COLLEGE October 23, 2019



#### **Project Team:**

Architect: LPAS

Project / Construction Manager: Critical Solutions, Inc.

Contractor: TBD

### **Project Description:**

The new Academic Support and Office building will be built in the location of existing buildings 2100 & 2200. The project will consist of the following elements and programs: English Center incorporating classrooms, computer lab, tutoring and study areas. Math Center incorporating classrooms, labs and the Math X program. Computer Sciences Center including computer labs, networking, maker space and open labs with the expanded of library functions including reference desk, study areas, computer lab, expanded staff offices and library operational support spaces. Faculty Offices Dean's Suite and Student gathering, and support spaces will also be located in the building.


### **Project Update:**

Schematic Design Phase was completed in early September 2019. Design Development phase has kicked off with Use Group and technical meetings taking place in early October 2019. Meetings with DSA and Livermore Fire have occurred in late August/September 2019.

Programming:	Complete
Schematic Design:	Complete
Design Development:	10/2019
Construction Documents:	05/2020
DSA Permit Approval:	TBD
Construction Start:	TBD
Occupancy:	TBD

### PROJECT PROGRESS REPORT Public Safety Complex/AMT

# LAS POSITAS COLLEGE October 23, 2019

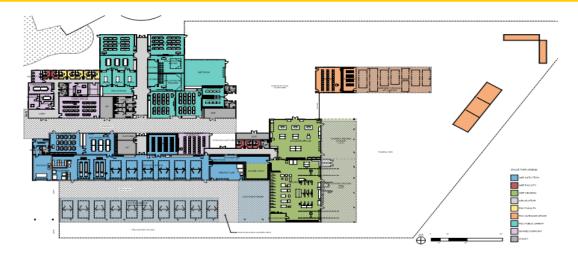

#### **Project Team:**

**Architect**: Lionakis

Project / Construction Manager: Critical Solutions, Inc.

Contractor: TBD

### **Project Description:**

The new Public Safety Center/Advanced Manufacturing and Transportation Facilities (PSC/AMT) will replace outdated facilities in Buildings 600A, 800 and 2200. The Public Safety programs will be located in the New Building 3400 and will include, the Administration of Justice, Fire Service Technology and Emergency Medical Services programs. A Risk Management Training apparatus, is planned as part of the Fire Service Technology program.

The Advanced Manufacturing and Transportation programs will be located in the New Building 3500, which will include Auto Technology, Advanced Manufacturing and the Welding Technology programs. There will be shared support for both programs that include Faculty Offices, Conference and Student gathering spaces

### **Project Update:**

Schematic Design progress is nearly complete. The team is reviewing the initial construction cost estimate (ICCE) with potential adjustments to meet the current approved budget for the project. Design Development Phase is anticipated to start in November 2019 with additional User Group and technical meetings with design team and their subconsultants.

Programming:	Complete
Schematic Design:	10/2019
Design Development:	12/2020
<b>Construction Documents:</b>	07/2020
DSA Permit Approval:	TBD
Construction Start:	TBD
Occupancy:	TBD

### PROJECT PROGRESS REPORT AG Science: Horticulture Project

# LAS POSITAS COLLEGE October 23, 2019





### **Project Team:**

**Architect**: ATI-AC Martin, Inc.

Construction Manager: Roebbelen (RCMS)

Contractor: TBD

#### **Project Description:**

The New Horticulture Facility will replace the facilities currently located in Building 800 and located outdoors and be located near the Maintenance and Operations facility and the Track and Field at the upper NE part of campus. The project includes, a parking area for up to 60 spaces for faculty and students. The Horticulture Facility includes a classrooms, Labs, offices and resource area, a greenhouse, shade structures. The outdoor growing areas will have soil bins, equipment storage and an outdoor learning patio.

### **Project Update:**

Architectural Programming Phase: The Design Team held several meetings with the User Group to develop project programming, provided preliminary sustainable checklist, conceptual estimate and refined conceptual site and building layout per User Group meetings. Schematic Design/Design Development Phase will begin in late October 2019, with the continuation of User Group meetings.

Programming:	Complete
Schematic Design:	10/2019
Design Development:	10/2019
Construction Documents:	02/2020
DSA Permit Approval:	TBD
Construction Start:	TBD
Occupancy:	TBD

### PROJECT PROGRESS REPORT AG Science: Viticulture Project

### LAS POSITAS COLLEGE October 23, 2019





#### **Project Team:**

**Architect**: tBP/Architecture

Project/Construction Manager: Roebbelen (RCMS)

Contractor: TBD

#### **Project Description:**

The New Viticulture Facility will replace the existing facilities currently located in/outside of Building 800. The Viticulture Facility will be located at the main entrance off the Campus Hill Road. This new roadway will connect the new facilities into the existing campus. The new facility will be developed at a higher elevation allowing for expansive views. The project will be include general site grading and utility infrastructure; New Roadway and Pedestrian pathways connecting to the existing campus. A Visitor Center with Tasting room, visitor Parking and clear paths of travel, A Winemaking Facility including classrooms and Labs, office and resource areas, Crush pad, Equipment storage, cold storage, and an Outdoor Patio.

### **Project Update:**

Design Proposals received in August 2019. Interviews were held on August 23, 2019. The committee recommended to award Design Services to tBP/Architecture. The Board approved the contract at the September 2019 Board Meeting. Upcoming, is the project kick-off meeting for infrastructure portion of the project

Programming:	10/2019
Schematic Design:	TBD
Design Development:	TBD
<b>Construction Documents:</b>	TBD
DSA Permit Approval:	TBD
Construction Start:	TBD
Occupancy:	TBD

# PROJECT PROGRESS REPORT Temporary Office Complex - Faculty Office Relocation Village

# LAS POSITAS COLLEGE October 23, 2019



**Project Team:** 

Architect: LPAS

Construction Manager: Critical Solutions, Inc.

Contractor: TBD

### **Project Description:**

The project includes providing modular buildings to accommodate ~ 75 faculty offices, conference rooms, and support spaces. In addition, a modular restroom unit will be provided to support the occupants. A raised, covered walkway with ramps will be provided to connect the modular buildings and modular restroom unit.

### **Project Update:**

Design Services with LPAS was approved at the October 2019 Board Meeting. Contracts to be issued in late October, with project kick-off meeting to happen in early November 2019.

Programming:	TBD
Schematic Design:	TBD
Design Development:	TBD
Construction Documents:	TBD
DSA Permit Approval:	TBD
Construction Start:	TBD
Occupancy:	TBD

### PROJECT PROGRESS REPORT Soccer Field Replacement Project

# LAS POSITAS COLLEGE October 23, 2019





#### **Project Team:**

Architect: Verdi Design, Inc.

Project/Construction Manager: Roebbelen (RCMS)

Contractor: Valley Precision Grading, Inc.

### **Project Description:**

The existing synthetic turf soccer field at Las Positas College is approximately 11+ years old. The project will remove and dispose of the existing synthetic turf, removal and disposal of the existing shock/drain pad beneath the turf and correct, as needed, the existing permeable base. Install new shock/drain pad, and complete the installation of the new turf product, including permeate NCAA/FIFA lines and marking for soccer and school logo. New removable bollards and protective netting will be installed for safety measures.

### **Project Update:**

Demolition of the existing field is complete. Grading for new turf is completed. Currently installing fabric, pad and turf. Upcoming is install of infill, bollards and netting, followed by clean-up and punch list.

Design	Completed
Pre-Construction Meeting	08/2019
Construction Start	08/2019
Final Completion	10/2019
Occupancy	11/2019

### PROJECT PROGRESS REPORT B2400 AV Wall Upgrade Room 2420

# LAS POSITAS COLLEGE October 23, 2019



### **Project Team:**

**Architect**: ATI Architects and Engineers **Construction Manager**: Roebbelen (RCMS)

Contractor: TBD

### **Project Description:**

The existing audio-visual system in Room B2420 is comprised of three projectors and a screen which includes AV controls at the lectern. The existing system will be replaced with LED flat panel system, movable lectern, upgraded speakers and cameras.

### **Project Update:**

Design and DSA permitting completed, Pre-Bid Conferences were completed, Bidding is currently under review. Potential Board Approval in November 2019, with Construction to happen during the Winter Break.

Design:CompletedDSA Permit Approval:CompletedBidding Phase:10/2019Construction:Winter BreakOccupancy:Spring Semester

# PROJECT PROGRESS REPORT Small Bond Projects

# LAS POSITAS COLLEGE October 23, 2019

### **Project Description:**

Meditation/ Prayer Room:

The renovation of a unused space within Bldg. 2400 is being converted to a meditation/prayer space for students, faculty and staff to use when needed.

Project was completed in August 2019

Locker Replacement PE Complex:

The existing men's and woman's team room lockers do not support the current requirements for programs utilizing the rooms. Current scope is to remove existing lockers and surplus to another facility, removal of the existing curbs for new locker installation.

Project was completed in September 2019

Tutoring Center Furniture Refresh

Portions of the existing furniture with in the Tutoring Center in B2400 will be replaced with new furniture, while existing furniture will be repurposed into other locations within the Tutoring center.

Project was completed in September 2019

Athletic Fields Feasibility Study:

The college engaged Verdi Design, Inc. to collaborate and produce a Feasibility study to determine if the proposed site can accommodate the athletic fields and supporting facilities desired by the college. Through a collaborative process with the college faculty and staff a desired program was established, conceptual layouts were prepared, and cost estimate provided. This feasibility study has been shared with the Design teams for the Public Safety Complex/AMT project and the AG SCI: Horticulture project for their use and information during the design phase of the projects.

Project was completed in July 2019

B1600 Architectural Barriers Project – Feasibility Study:

The project is intended to identify the appropriate infrastructure upgrades, renovations, and alterations of the existing Student Services and Administrations building. The college has identified four key areas of the building making spaces more secured and more functional for the way the college operates. These spaces include the Information/Reception window on the first floor, Admissions & Records, Financial Aid and finally Counseling Services.



# IT BOND PROJECT UPDATE

CHABOT-LAS POSITAS CCD October 23, 2019

# IMPLEMENTATION OF LATEST INDUSTRY STANDARD 802.11AC DATA WIRELESS EQUIPMENT

- Exterior wireless augmentation completed at LPC at outside seating areas by Library/Science, B1600/B800, AmphiTheatre, B1000/B400, CCA.
- LPC PE fields under investigation.
- Chabot PE fields and other outside congregation areas under review.



# DISTRIBUTED ANTENNAE SYSTEM (DAS) FOR IMPROVED CELLULAR COVERAGE INSIDE BUILDINGS

- IBWave Design for 6 sector design across all carriers is being built in ION-E CANs.
- All TENs online and functional.
- IPOI and GPS switching equipment installed.
- AT&T Transport in place, waiting for service initiation.
- Verizon racks and power ready for MPOE build.
- B1900A enhancements for carrier connectivity complete.
- Fiber reterminations planned in select locations.
- UPSes installed in all available IDFs.



## CHABOT NETWORK UPGRADES

### **Recent Activity**


- Buildings completed with new fiber (data) and copper (voice) backbones
- Buildings upgraded to 10G connectivity: 304, 1600, 3900, 2300.
- Replacement continues of 45+ switches across Chabot campus with new Cisco 3650 switches.
- Planning for deployment of 9407 chassis switches underway

# CHABOT FIREPOWER DEPLOYMENT

- Cisco FirePower NetGen firewall rollout to provide a more robust security environment for the network traffic.
- Architecture is being formulated with campus IT input.
- Prototype configuration is planned for summer of 2019.

# CHABOT MPOE REPLACEMENT

- Design review in progress.
- Coordination with AT&T engineering for new campus provisioning has occurred.
- Expect to submit to DSA in Fall of 2019, with construction in 2020.
- After construction, up to a year of work is required to convert voice and data services and add DAS system.

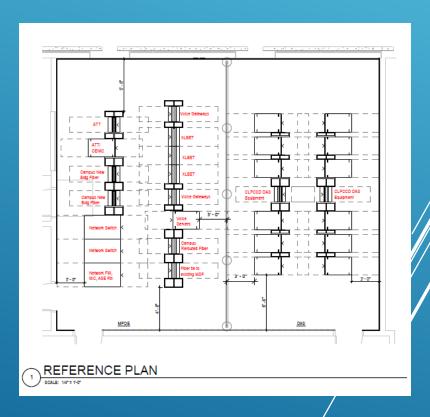

# FMO PROJECT SUPPORT

### Chabot

- New Bio building walkthroughs
- FA Upgrade fiber installation
- New Library building A&E coordination and user group meetings
- B500 computer labs and small cabling in various buildings.

### LPC

- New B2100 Building design meetings
- PSC/AMT design meetings
- FMO trailer add
- B1600, B803 recabling.



### **Chabot-Las Positas Community College District**

### Facilities Modernization Program Funded by Measure A Data Date: September 30, 2019

**Project Budget Summary** 

(A)

(B)

(C)

(D)

		()	ν-/	( )	\ /
Fund	Fund Description	Current Budget	Actual Expenditures to Date	Unpaid Commitments	Remaining Budget A - (B+C) = D
DISTRICTWIDE TOTA	ALS	136,000,000	21,119,737	3,214,982	111,665,282
CHABOT COLLEGE T	OTALS	407,000,000	6,673,754	10,634,377	389,691,868
LAS POSITAS COLLE	GE TOTALS	407,000,000	5,188,391	13,631,153	388,180,456
PROGRAM TOTALS		950,000,000	32,981,882	27,480,512	889,537,606



### **Chabot-Las Positas Community College District**

### Facilities Modernization Program Funded by Measure A Data Date: September 30, 2019

Project Budget Summary

(A) (B) (C) (D)

		(A)	(B)	(0)	(D)
Fund	Fund Description	Current Budget	Actual Expenditures to Date	Unpaid Commitments	Remaining Budget A - (B+C) = D
DISTRICT	WIDE				
561010	Information Technology & Tech Upgrades	51,300,000	4,884,097	287,946	46,127,958
561011	Classroom, Lab Equipment, Chabot College	-	4,214,779	355,356	(4,570,134)
561012	Classroom, Lab Equipment, Las Positas College	-	6,042,910	665,961	(6,708,871)
561020	Deferred Maint & Repairs: Roofs, HVAC, Small Projects	16,000,000	738,878	895,951	14,365,171
561021	Deferred Maint & Repairs: Small Projects, CC	1,000,000	-	-	1,000,000
561022	Deferred Maint & Repairs: Small Projects, LPC	1,000,000	-	-	1,000,000
561025	M&O Equipment	1,000,000	457,500	120,489	422,011
561027	Campus Security Equipment	150,000	-	-	150,000
561030	Program Level Services, District	57,832,300	2,058,691	813,363	54,960,246
561040	Dublin Education Center/Contract Ed/TVOS	1,182,583	392,812	853	788,918
561042	Dublin Education Center Phase III	17,417	1,519	15,898	0
561060	Energy Projects	3,000,000	1,758,353	1,889	1,239,758
561090	2018 Facilities Master Plan Update	750,000	570,199	57,277	122,525
561099	District Contingency Fund 5%	2,767,700	-	-	2,767,700
DISTRICTW	IDE TOTALS	136,000,000	21,119,737	3,214,982	111,665,282



**CHABOT COLLEGE TOTALS** 

# Chabot-Las Positas Community College District Facilities Modernization Program

Funded by Measure A

Data Date: September 30, 2019

**Project Budget Summary** 

		(A)	(B)	(C)	(D)
Fund	Fund Description	Current Budget	Actual Expenditures to Date	Unpaid Commitments	Remaining Budget A - (B+C) = D
CHABOT (	COLLEGE				
562100	Library Building 100	99,027,848	808,733	7,017,921	91,201,195
562109	Demolish B100	1,712,304	-	-	1,712,304
562160	Advanced Mfg, Applied Tech & Bus	35,216,956	-	-	35,216,956
562209	Demolish B200	471,936	-	-	471,936
562210	Biology / Faculty Building 2100 Ph. 2	49,049,755	-	-	49,049,755
562230	College Center	100,686,370	-	-	100,686,370
562239	Demolish B2300	908,616	-	-	908,616
562249	Demolish B2400	129,792	-	-	129,792
562300	MPOE Relocation and Renovation Project	2,178,635	171,193	124,507	1,882,935
562340	Vehicle Storage	3,895,353	-	-	3,895,353
562370	Early Childhood Lab School	3,547,126	-	-	3,547,126
562380	Event Center & Campus Safety Renovation	5,768,115	-	-	5,768,115
562500	Athletic Fields - Baseball	12,771,748	505,179	859,600	11,406,969
562501	Athletic Fields - Football	10,642,500	-	-	10,642,500
562510	Fire Technology - Hayward Training Facility	20,000,000	23,419	1,301	19,975,281
562540	Classroom/Lab Equipment & Library Materials	40,000,000	1,542,923	267,193	38,189,884
562560	CC Project & Construction Management	6,000,000	955,077	1,233,546	3,811,377
562561	Facilities Management Office Project	-	-	-	-
562600	Campus Security	1,793,819	950,171	120,827	722,820
562601	Campuswide FA PA Upgrade	3,028,550	1,691,735	988,282	348,533
562602	Campuswide LED Lighting	177,631	25,324	21,200	131,107
562610	Parking & Pathways - Lots G, E & F	556,150	-	-	556,150
562699	Unallocated Bond for Projects, CC	9,436,796	-	-	9,436,796

407,000,000

6,673,754

10,634,377

389,691,868



LAS POSITAS COLLEGE TOTALS

## Chabot-Las Positas Community College District

# Facilities Modernization Program Funded by Measure A Data Date: September 30, 2019

**Project Budget Summary** 

(A) (C) (D) (B) Current **Actual Expenditures Unpaid Remaining Budget Fund Description** to Date A - (B+C) = D**Fund** Budget Commitments LAS POSITAS COLLEGE 563700 Library, Offices, Labs, Classrooms B2100 99,417,507 1,224,598 5,487,752 92,705,157 647.750 563701 AV Upgrades B2420 41.747 19.625 586.378 Fire Technology/EMS/Paramedic Building 3400 563710 23,051,613 23,051,613 563715 Public Safety Complex/AMT Project (3,769,179)195,400 3,573,779 563720 Auto Tech / Welding Tech B3500 32.806.210 32.806.210 563730 Campus Vehicular Circulation 5,071,280 37,509 571 5,033,200 563740 Athletic Fields 21,730,328 29,850 21,700,478 563741 Soccer Field Replacement Project 665,950 30,450 1,127,425 (491,925)STEAM - Sciences Building 563750 85.345.051 85.345.051 563755 STEAM - Arts Building 33.692.937 33.692.937 563800 Temporary Relocatable Offices Project 4,645,057 7,033 4,638,025 Agricultural Sciences - Horticulture 4,728,123 563810 5,213,276 24,252 460,900 563811 Agricultural Sciences - Viticulture 9,818,372 273 25,133 9,792,966 563830 Classroom/Lab Equipment & Library Materials 40.000.000 1.374.330 445.687 38.179.983 563860 LPC Project & Construction Management 6,000,000 1,524,762 2,354,387 2,120,851 563900 Campus Security 5,000,000 688,510 134,914 4,176,576 563912 Demolish B600 & B800 1.076.024 1.076.024 563920 **EIR Services** 750,000 9,679 978 739,343 563930 Infrastructure HW/CW/Electric 10,684,153 10,684,153 Renovate B1800 9,087,517 9,087,517 563999 Unallocated Bond for Projects, LPC 12,296,975 12,296,975

407,000,000

5,188,391


13,631,153

388,180,456



# Chabot-Las Positas Community College District Facilities Modernization Program Funded by Measure A Data Date: September 30, 2019

Cash Flow Report

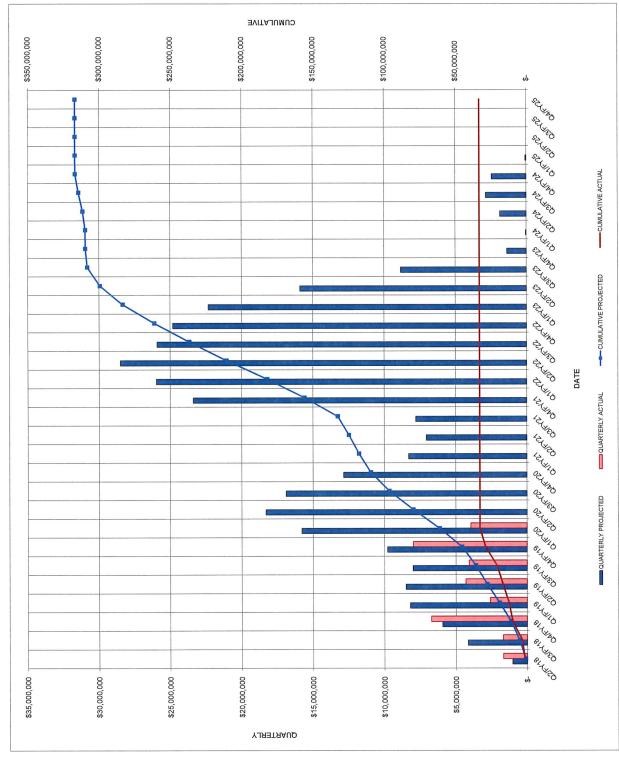

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 1

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 561010 INFORMATION TECH & TECH UPGRADES

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
2111 2303		MANAGEMENT OVERTIME	123,874.20 .00				92,905.65 -455.84	25 ***
TOTAL		Classified Salaries	123,874.20	10,778.69	31,424.39	.00	92,449.81	25
3221 3320 3321 3421 3520 3521 3620	719998 719998 719998 719998 719998	PERS-CLASS ADMINISTRATORS OASDHI OTHER CLASS EMPLOYEES OASDHI CLASS MANAGERS H & W CLASS MANAGERS SUI OTHER CLASS EMPLOYEES SUI CLASS MANAGERS WCI OTHER CLASS EMPLOYEES	24,428.70 .00 9,212.40 18,775.80 .00 62.10	32.54 784.41 1,590.96 .23 5.16	32.54 2,353.22 4,772.88 .23 15.48	.00 .00 .00 .00	18,321.39 -32.54 6,859.18 14,002.92 23 46.62 -5.97	25 *** 26 25 *** 25 ***
3621		WCI CLASS MANAGERS	1,635.30		•	The state of the s	1,230.00	25
TOTAL		Fringe Benefits	54,114.30	4,590.14	13,692.93	.00	40,421.37	25
5110 5541 5641 5647 5851 5897 5898	719998 719998 719998 719998 719998 719998	PROFESSIONAL SERVICES DATA COMMUNICATIONS MAINTENANCE - SOFTWARE EQUIP MAINT - ALL OTHER SERVIC SOFTWARE LICENSES ENTERPRISE HARDWARE/SOFTWARE L HARDWARE/SOFTWARE MULTI-YR AGR Other Operating Expenses & Ser	.00 .00 .00 .00 .00 .00	1,363.15 .00 .00 .00 .00 .00	4,089.45 43,799.79 37,567.41 69,107.45 22,552.35 7,325.03	18,385.75 8,147.58 .00 669.36 .00 .00	•	* * * * * * * * * * * * * * * * * * *
	719998 719998	BUILDING ALTERATIONS & IMPROV EQUIPMENT <\$1000 EQUIPMENT \$1000 to 4999.99 EQUIPMENT >\$5000 CAPITALIZED Capital Expenses	.00	5,211.23 .00 .00	17,976.43 131,622.99 55,656.75	.00 .00 15,308.27	-1,942.00 -17,976.43 -131,622.99 -70,965.02 -222,506.44	* * * * * * * * * * * *
TOTAL 50100	ORGANIZ.	ATION BOND FUND DISTRICT-WIDE						
TOTAL TOTAL		Labor Expenditures	177,988.50 .00		45,117.32 389,491.25		132,871.18 -512,218.86	25 ***
NET			-177,988.50	-23,685.21	-434,608.57	-122,727.61	379,347.68	313

Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 2

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND:

561010 INFORMATION TECH & TECH UPGRADES

PRED ORG: 5500 BOND FUND RESTRICTED BOND FUND DISTRICT-WIDE ORG: 50100

ACCT PROG	ACCOUNT TIT	LE		ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
TOTAL FUND 561010	INFORMATION T UPGRADES	PECH &	TECH						
TOTAL TOTAL	Labor Expenditures			177,988.50 .00	•			132,871.18 -512,218.86	25 ***
NET				-177,988.50	-23,685,21	-434,608.57	-122,727.61	379,347.68	313

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 3

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 561011 CLASSROOM, LAB EQUIPMENT, CC

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5110 5641 5647 5851	719998 719998	PROFESSIONAL SERVICES MAINTENANCE - SOFTWARE EQUIP MAINT - ALL OTHER SERVIC SOFTWARE LICENSES	.00 .00 .00	.00 .00 1,519.00 .00	20,405.73 45,528.21	.00 68,841.86	-67,943.85 -20,405.73 -114,370.07 -41,186.68	* * * * * * * * *
TOTAL		Other Operating Expenses & Ser	.00	1,519.00	142,988.42	100,917.91	-243,906.33	***
6120 6201 6401 640101 TOTAL	719998 719998	SITE IMPROVEMENTS BUILDING ALTERATIONS & IMPROV EQUIPMENT <\$1000 EQUIPMENT \$1000 to 4999.99 Capital Expenses	.00 .00 .00	.00 12,731.00 12,433.19 110,553.71	12,731.00 32,705.73 138,707.92	30.51 26,778.56 99,674.02	-44,323.58 -12,761.51 -59,484.29 -238,381.94	* * * * * * * * * * * *
	ORGANIZ		.00	133,717.30	175,042.50	173,300.34	334, 331.32	
50100		BOND FUND DISTRICT-WIDE						
TOTAL		Expenditures	.00	137,236.90	322,631.40	276,226.25	-598,857.65	***
NET			.00	-137,236.90	-322,631.40	-276,226.25	598,857.65	***
TOTAL 561011		CLASSROOM, LAB EQUIPMENT, CC						
TOTAL		Expenditures	.00	137,236.90	322,631.40	276,226.25	-598,857.65	***
NET			.00	-137,236.90	-322,631.40	-276,226.25	598,857.65	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM PAGE: 4

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D
FUND: 561012 CLASSROOM, LAB EQUIPMENT, LPC

PRED ORG: 5500 BOND FUND RESTRICTED
ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5102 5110 5641 5647 5851 5898	719998 719998 719998 719998	STAFF TRAINING & WORKSHOPS PROFESSIONAL SERVICES MAINTENANCE - SOFTWARE EQUIP MAINT - ALL OTHER SERVIC SOFTWARE LICENSES HARDWARE/SOFTWARE MULTI-YR AGR	.00 .00 .00 .00	.00 .00 .00	.00 12,277.73 32,966.48 1,353.31	176,482.56 .00 125,647.41 .00	-27,014.00 -176,482.56 -12,277.73 -158,613.89 -1,353.31 -56,669.45	* * * * * * * * * * * *
TOTAL		Other Operating Expenses & Ser	.00	.00	103,266.97	329,143.97	-432,410.94	***
6201 6202 6401 640101	719998 719998	BUILDING ALTERATIONS & IMPROV DESIGN EQUIPMENT <\$1000 EQUIPMENT \$1000 to 4999.99	.00 .00 .00	4,080.00 .00	10,000.00	13,747.77 16,066.40	-9,031.17 -23,747.77 -16,066.40 -63,236.10	* * * * * * * * *
TOTAL		Capital Expenses	.00	12,855.00	•	,	-112,081.44	***
TOTAL 50100	ORGANIZ	ATION BOND FUND DISTRICT-WIDE						
TOTAL		Expenditures	.00	12,855.00	155,057.48	389,434.90	-544,492.38	***
NET			.00	-12,855.00	-155,057.48	-389,434.90	544,492.38	***
TOTAL 561012		CLASSROOM, LAB EQUIPMENT, LPC						
TOTAL		Expenditures	.00	12,855.00	155,057.48	389,434.90	-544,492.38	***
NET			.00	-12,855.00	-155,057.48	-389,434.90	544,492.38	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 5

FINANCE MGR:

FUND:

COAS: 1 Chabot - Las Positas C C D

561020 DEF MAINT & REP: ROOFS, HVAC, SM PROJ

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
2101 2303		REGULAR	.00	.00	2,475.84		-2,475.84	***
2303	/19998	OVERTIME	.00	.00	1,831.68	.00	-1,831.68	***
TOTAL		Classified Salaries	.00	.00	4,307.52	.00	-4,307.52	***
3220	719998	PERS OTHER CLASS EMPLOYEES	.00	.00	284.81	.00	-284.81	***
3320		OASDHI OTHER CLASS EMPLOYEES	.00	.00	301.43		-301.43	***
3420		H & W OTHER CLASS EMPLOYEES	.00	.00	181.29		-181.29	***
3520		SUI OTHER CLASS EMPLOYEES	.00	.00	2.16		-2.16	***
3620		WCI OTHER CLASS EMPLOYEES	.00	.00	56.37	.00	-56.37	***
3720	719998	ARS-CLASS OTHER	.00	.00	15.47	.00	-15.47	***
TOTAL		Fringe Benefits	.00	.00	841.53	.00	-841.53	***
5110	719998	PROFESSIONAL SERVICES	.00	-8,964.05	48,719.00	5,000.00	-53,719.00	***
5620	719998	M & O VENDOR REPAIRS	.00	17,200.00	17,200.00		-42,150.00	***
TOTAL		Other Operating Expenses & Ser	.00	8,235.95	65,919.00	29,950.00	-95,869.00	***
6120	719998	SITE IMPROVEMENTS	.00	38,266.20	208,514.47	687,498.26	-896,012.73	***
6201	719998	BUILDING ALTERATIONS & IMPROV	.00	106,127.45	121,283.94		-241,036.87	***
6210	719998	CONSTRUCTION MANAGEMENT	.00	7,420.00	6,230.00		-6,230.00	***
6215	719998	SPECIALITY CONSULTING	.00	.00	.00		-28,681.36	***
6401	719998	EQUIPMENT <\$1000	.00	.00	.00	•	-17,538.63	***
TOTAL		Capital Expenses	.00	151,813.65	336,028.41	853,471.18	-1,189,499.59	***
TOTAL 50100	ORGANIZ	ATION BOND FUND DISTRICT-WIDE						
TOTAL		Labor	.00	.00	E 140 05	0.0	F 140 0F	التيلييات
TOTAL		Expenditures	.00	160,049.60	5,149.05 401,947.41		-5,149.05 -1,285,368.59	***
ATT		-		,				
NET			.00	-160,049.60	-407,096.46	-883,421.18	1,290,517.64	***

Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 6

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND:

561020 DEF MAINT & REP: ROOFS, HVAC, SM PROJ

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT I	PROG ACCOUN'	T TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
TOTAL FUI 561020		& REP: ROOFS,HVAC,SM						
TOTAL TOTAL	Labor Expenditure	es	.00		.,	•	-5,149.05 -1,285,368.59	* * * * * *
NET			.00	-160,049.60	-407,096.46	-883,421.18	1,290,517.64	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 7

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 561025 M&O EQUIPMENT

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6201 6401 640101	719998 719998 719998	SITE IMPROVEMENTS BUILDING ALTERATIONS & IMPROV EQUIPMENT <\$1000 EQUIPMENT \$1000 to 4999.99 EQUIPMENT >\$5000 CAPITALIZED Capital Expenses	.00	.00 4,106.80 2,921.84 26,578.13	2,921.84 57,738.43	.00 79,736.10	.00 .00 -29,644.78 -2,921.84 -137,474.53	*** *** *** ***
TOTAL O	RGANIZ	ATION BOND FUND DISTRICT-WIDE						
TOTAL		Expenditures	.00	30,267.10	60,584.50	109,456.65	-170,041.15	***
NET			.00	-30,267.10	-60,584.50	-109,456.65	170,041.15	***
TOTAL F1 561025	UND	M&O EQUIPMENT						
TOTAL		Expenditures	.00	30,267.10	60,584.50	109,456.65	-170,041.15	***
NET			.00	-30,267.10	-60,584.50	-109,456.65	170,041.15	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM PAGE: 8

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND:

561030 PROGRAM LEVEL SERVICES, DISTRICT

PRED ORG: BOND FUND RESTRICTED 5500 ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
2101 2111 2131 2303	719998 719998	REGULAR MANAGEMENT CONFIDENTIAL OVERTIME	338,752.31 217,948.00 79,370.59 .00	14,166.67 5,919.12	61,935.64 42,500.01 17,757.36 3,760.64	.00	276,816.67 175,447.99 61,613.23 -3,760.64	18 20 22 ***
TOTAL		Classified Salaries	636,070.90	43,027.78	125,953.65	.00	510,117.25	20
3220 3221 3320 3321 3420 3421 3520 3521 3620 3621 3921EX	719998 719998 719998 719998 719998 719998 719998 719998	PERS OTHER CLASS EMPLOYEES PERS-CLASS ADMINISTRATORS OASDHI OTHER CLASS EMPLOYEES OASDHI CLASS MANAGERS H & W OTHER CLASS EMPLOYEES H & W CLASS MANAGERS SUI OTHER CLASS EMPLOYEES SUI CLASS MANAGERS WCI OTHER CLASS EMPLOYEES WCI CLASS MANAGERS EXP ALLWNCE CLASS MGR	82,455.39 42,980.00 31,992.37 13,138.00 131,448.85 28,251.50 211.98 109.00 5,522.31 2,877.00	204.85 7,576.31 3,168.69 14.52 7.08 377.70	15,232.30 4,053.26 6,174.43 2,362.85 22,467.26 9,506.07 42.04 21.24 1,092.13 556.21 510.00	.00 .00 .00 .00 .00 .00	67,223.09 38,926.74 25,817.94 10,775.15 108,981.59 18,745.43 169.94 87.76 4,430.18 2,320.79 -510.00	18 9 19 18 17 34 20 19 20
TOTAL		Fringe Benefits	338,986.40		62,017.79	•	276,968.61	18
5110 5641 5701 5730 5851 TOTAL 6210	719998 719998 719998 719998	PROFESSIONAL SERVICES MAINTENANCE - SOFTWARE ANNUAL FISCAL AUDIT ATTORNEY FEES SOFTWARE LICENSES Other Operating Expenses & Ser CONSTRUCTION MANAGEMENT Capital Expenses	.00	.00 .00 9,450.00 .00 .00 9,450.00 15,198.50	.00 .00 9,450.00 .00 20,740.59 30,190.59 34,747.50	447.00 .00 20,000.00 .00 36,942.00 775,371.00	-16,495.00 -447.00 -9,450.00 -20,000.00 -20,740.59 -67,132.59 -810,118.50	*** *** ***  ***  ***
TOTAL 50100	ORGANIZ	ATION BOND FUND DISTRICT-WIDE						
TOTAL TOTAL		Labor Expenditures	975,057.30 .00	60,436.87 24,648.50	187,971.44 64,938.09		787,085.86 -877,251.09	19 ***
NET			-975,057.30	-85,085.37	-252,909.53	-812,313.00	90,165.23	109

Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 9

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND:

561030 PROGRAM LEVEL SERVICES, DISTRICT

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT	PROG	ACCOUNT TITLE		ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
TOTAL : 561030		PROGRAM LEVEL DISTRICT	SERVICES,						
TOTAL TOTAL		Labor Expenditures		975,057.30 .00	,			787,085.86 -877,251.09	19 ***
NET				-975,057.30	-85,085.37	-252,909.53	-812,313.00	90,165.23	109

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 10

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 561040 DUBLIN ED CENTER/CONTRACT ED/TVOS

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT P	ROG ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5647 71	9998 EQUIP MAINT - ALL OTHER SERVIC	.00	201.87	316.70	46.07	-362.77	***
TOTAL	Other Operating Expenses & Ser	.00	201.87	316.70	46.07	-362.77	***
6401 71	9998 EQUIPMENT <\$1000	.00	.00	.00	806.77	-806.77	***
TOTAL	Capital Expenses	.00	.00	.00	806.77	-806.77	***
TOTAL ORG	ANIZATION BOND FUND DISTRICT-WIDE Expenditures	.00	201.87	316.70	852.84	-1,169.54	***
NET	-	.00	-201.87			1,169.54	***
TOTAL FUN 561040	D DUBLIN ED CENTER/CONTRACT ED/TVOS						
TOTAL	Expenditures	.00	201.87	316.70	852.84	-1,169.54	***
NET		.00	-201.87	-316.70	-852.84	1,169.54	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM PAGE: 11

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND:

561042 DUBLIN EDUCATION CENTER PHASE III

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5647 719998	B EQUIP MAINT - ALL OTHER SERVIC	.00	271.91	547.17	15,898.11	-16,445.28	***
TOTAL	Other Operating Expenses & Ser	.00	271.91	547.17	15,898.11	-16,445.28	***
TOTAL ORGANIZ 50100	ZATION BOND FUND DISTRICT-WIDE						
TOTAL	Expenditures	.00	271.91	547.17	15,898.11	-16,445.28	***
NET		.00	-271,91	-547.17	-15,898.11	16,445.28	***
TOTAL FUND 561042	DUBLIN EDUCATION CENTER PHASE						
TOTAL	Expenditures	.00	271.91	547.17	15,898.11	-16,445.28	***
NET		.00	-271.91	-547.17	~15,898.11	16,445.28	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 12

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 561060 ENERGY PROJECTS

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6241 71999	8 TESTS & INSPECTIONS	.00	.00	.00	1,889.14	-1,889.14	***
TOTAL	Capital Expenses	.00	.00	.00	1,889.14	-1,889.14	***
TOTAL ORGANI 50100	ZATION BOND FUND DISTRICT-WIDE						
TOTAL	Expenditures	.00	.00	.00	1,889.14	-1,889.14	***
NET		.00	.00	.00	-1,889.14	1,889.14	***
TOTAL FUND 561060	ENERGY PROJECTS						
TOTAL	Expenditures	.00	.00	.00	1,889.14	-1,889.14	***
NET		.00	.00	.00	-1,889.14	1,889.14	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 13

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 561090 2018 FACILITIES MASTER PLAN UPDATE

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5110	719998	PROFESSIONAL SERVICES	.00	2,400.00	2,400.00	23,300.00	-25,700.00	***
TOTAL		Other Operating Expenses & Ser	.00	2,400.00	2,400.00	23,300.00	-25,700.00	***
6215	719998	SPECIALITY CONSULTING	.00	2,388.75	4,488.75	33,976.50	-38,465.25	***
TOTAL		Capital Expenses	.00	2,388.75	4,488.75	33,976.50	-38,465.25	***
50100	ORGANIZ	BOND FUND DISTRICT-WIDE		4 500 55				
TOTAL		Expenditures	.00	•	,	,	-64,165.25	***
NET			.00	-4,788.75	-6,888.75	-57,276.50	64,165.25	***
TOTAL 1 561090		2018 FACILITIES MASTER PLAN UPDATE						
TOTAL		Expenditures	.00	4,788.75	6,888.75	57,276.50	-64,165.25	***
NET			.00	-4,788.75	-6,888.75	-57,276.50	64,165.25	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 14

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 562100 LIBRARY BUILDING 100

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50200 BOND FUND CHABOT COLLEGE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6202 6215 6241	719998	DESIGN SPECIALITY CONSULTING TESTS & INSPECTIONS	.00 .00 .00	113,803.09 .00 .00	.00	6,962,520.76 .00 .00	-7,246,335.10 .00 .00	* * * * * * * * *
TOTAL		Capital Expenses	.00	113,803.09	283,814.34	6,962,520.76	-7,246,335.10	***
TOTAL 6	ORGANIZ	ATION BOND FUND CHABOT COLLEGE						
TOTAL		Expenditures	.00	113,803.09	283,814.34	6,962,520.76	-7,246,335.10	***
NET			.00	-113,803.09	-283,814.34	-6,962,520.76	7,246,335.10	***
TOTAL 1 562100		LIBRARY BUILDING 100						
TOTAL		Expenditures	.00	113,803.09	283,814.34	6,962,520.76	-7,246,335.10	***
NET			.00	-113,803.09	-283,814.34	-6,962,520.76	7,246,335.10	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

170,710.86

\*\*\*

PAGE: 15

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 562300 MPOE REPLACEMENT PROJECT PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50200 BOND FUND CHABOT COLLEGE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6202 6222 6241 TOTAL	719998	DESIGN DSA PLAN CHECK TESTS & INSPECTIONS Capital Expenses	.00	.00	42,954.00 .00 3,250.00 46,204.00	123,381.86 .00 1,125.00 124,506.86	-166,335.86 .00 -4,375.00 -170,710.86	* * * * * * * * *
TOTAL 0	ORGANIZ	ATION BOND FUND CHABOT COLLEGE						
TOTAL		Expenditures	.00	2,388.75	46,204.00	124,506.86	-170,710.86	***

TOTAL FUND

562300

NET

MPOE REPLACEMENT PROJECT

TOTAL Expenditures .00 2,388.75 46,204.00 124,506.86 -170,710.86 \*\*\*
NET .00 -2,388.75 -46,204.00 -124,506.86 170,710.86 \*\*\*

-2,388.75

-46,204.00

-124,506.86

.00

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 16

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 562500 ATHLETIC FIELDS - BASEBALL

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50200 BOND FUND CHABOT COLLEGE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6202 6210 6215 6222	719998 719998	DESIGN CONSTRUCTION MANAGEMENT SPECIALITY CONSULTING DSA PLAN CHECK	.00 .00 .00	-130,753.96 .00	27,025.40 .00	501,937.11 299,430.60	-86,884.00 -528,962.51 -299,430.60 -3,600.00	* * * * * * * * *
TOTAL		Capital Expenses	.00	-102,102.06	59,277.30	859,599.81	-918,877.11	***
TOTAL 50200	ORGANIZ	ATION BOND FUND CHABOT COLLEGE						
TOTAL		Expenditures	.00	-102,102.06	59,277.30	859,599.81	-918,877.11	***
NET			.00	102,102.06	-59,277.30	-859,599.81	918,877.11	***
TOTAL 562500		ATHLETIC FIELDS - BASEBALL						
TOTAL		Expenditures	.00	-102,102.06	59,277.30	859,599.81	-918,877.11	***
NET			.00	102,102.06	-59,277.30	-859,599.81	918,877.11	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 17

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 562510 FIRE TECH-HAYWARD TRAINING FACILITY

PRED ORG: 5500 BOND FUND RESTRICTED
ORG: 50200 BOND FUND CHABOT COLLEGE

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5730 71999	8 ATTORNEY FEES	.00	1,302.00	1,302.00	1,300.50	-2,602.50*	***
TOTAL	Other Operating Expenses & Ser	.00	1,302.00	1,302.00	1,300.50	-2,602.50	***
TOTAL ORGANI 50200	ZATION BOND FUND CHABOT COLLEGE						
TOTAL	Expenditures	.00	1,302.00	1,302.00	1,300.50	-2,602.50	***
NET		.00	-1,302.00	-1,302.00	-1,300.50	2,602.50	***
TOTAL FUND 562510	FIRE TECH-HAYWARD TRAINING FACILITY						
TOTAL	Expenditures	.00	1,302.00	1,302.00	1,300.50	-2,602.50	***
NET		.00	-1,302.00	-1,302.00	-1,300.50	2,602.50	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM PAGE: 18

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND:

562540 CLASSROOM/LAB EQUIP & LIBRARY MAT'L

PRED ORG: 5500 BOND FUND RESTRICTED 50200 BOND FUND CHABOT COLLEGE ORG:

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
	PROTECTIVE CLOTHING & UNIFORMS EQUIP MAINT - ALL OTHER SERVIC	.00	4,592.44 .00	5,040.05 1,504.69	.00	-5,040.05 -1,504.69	* * * * * *
TOTAL	Other Operating Expenses & Ser	.00	4,592.44	6,544.74	.00	-6,544.74	***
6401 719998 640101 719998	LIBRARY BOOKS EQUIPMENT <\$1000 EQUIPMENT \$1000 to 4999.99 EQUIPMENT >\$5000 CAPITALIZED Capital Expenses	.00 .00 .00 .00	33,871.21 839.42 .00 .00	4,186.94 7,516.19 .00	3,502.99 12,877.79 47,657.06	-284,115.04 -7,689.93 -20,393.98 -47,657.06	* * * * * * * * * * * *
TOTAL ORGANIZ 50200	ATION BOND FUND CHABOT COLLEGE						
TOTAL	Expenditures	.00	39,303.07	168,810.93	197,589.82	-366,400.75	***
NET		.00	-39,303.07	-168,810.93	-197,589.82	366,400.75	***
TOTAL FUND 562540	CLASSROOM/LAB EQUIP & LIBRARY MAT'L						
TOTAL	Expenditures	.00	39,303.07	168,810.93	197,589.82	-366,400.75	***
NET		.00	-39,303.07	-168,810.93	-197,589.82	366,400.75	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM PAGE: 19

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 562560 CC PROJECT & CONSTRUCTION MGMNT

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50200 BOND FUND CHABOT COLLEGE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
2111	719998	MANAGEMENT	159,070.00	13,255.83	39,767.49	.00	119,302.51	25
TOTAL		Classified Salaries	159,070.00	13,255.83	39,767.49	.00	119,302.51	25
3221 3321 3421 3521 3621	719998 719998 719998	PERS-CLASS ADMINISTRATORS OASDHI CLASS MANAGERS H & W CLASS MANAGERS SUI CLASS MANAGERS WCI CLASS MANAGERS	31,369.00 10,547.00 20,920.00 80.00 2,100.00	995.93 1,429.37 6.63	7,842.54 2,987.80 4,288.11 19.89 520.44	.00 .00 .00 .00	23,526.46 7,559.20 16,631.89 60.11 1,579.56	25 28 20 25 25
TOTAL		Fringe Benefits	65,016.00	5,219.59	15,658.78	.00	49,357.22	24
4301	719998	OFFICE SUPPLIES	.00	109.84	592.17	815.15	-1,407.32	***
TOTAL		Supplies Expense	.00	109.84	592.17	815.15	-1,407.32	***
5110 5647 588402	719998	PROFESSIONAL SERVICES EQUIP MAINT - ALL OTHER SERVIC MOVING/RELOCATION EXPENSE	.00 .00 .00	.00	.00 130.35 .00	25,432.63 63.85 3,465.60	-25,432.63 -194.20 -3,465.60	* * * * * *
TOTAL		Other Operating Expenses & Ser	.00	.00	130.35	28,962.08	-29,092.43	***
620203 6210 6215 TOTAL	719998	DESIGN REPROGRAPHICS CONSTRUCTION MANAGEMENT SPECIALITY CONSULTING Capital Expenses	.00	.00	-835.39 32,177.39 .00 31,342.00	1,175,697.59 12,960.00	-9,745.89 -1,207,874.98 -12,960.00 -1,230,580.87	* * * * * * * * *
TOTAL 50200	ORGANIZ	ATION BOND FUND CHABOT COLLEGE						
TOTAL TOTAL		Labor Expenditures	224,086.00 .00	•		-	168,659.73 -1,261,080.62	25 ***
NET			-224,086.00	-18,611.04	-87,490.79	-1,229,016.10	1,092,420.89	588

Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 20

FINANCE MGR:

Chabot - Las Positas C C D COAS: 1 FUND:

562560 CC PROJECT & CONSTRUCTION MGMNT

PRED ORG: 5500 BOND FUND RESTRICTED 50200 BOND FUND CHABOT COLLEGE ORG:

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
TOTAL FUND 562560	CC PROJECT & CONSTRUCTION MGMNT						
TOTAL TOTAL	Labor Expenditures	224,086.00	18,475.42 135.62	•	.00 1,229,016.10	168,659.73 -1,261,080.62	25 ***
NET		-224,086.00	-18,611.04	-87,490.79	-1,229,016.10	1,092,420.89	588

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

1,435,135.66

PAGE: 21

FINANCE MGR:

NET

COAS: 1 Chabot - Las Positas C C D

FUND: 562600 CAMPUS SECURITY

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50200 BOND FUND CHABOT COLLEGE

ADJUSTED CURRENT PERIOD YEAR TO DATE BUDGET AVAILABLE % BGT ACCT PROG ACCOUNT TITLE BUDGET ACTIVITY ACTIVITY RESERVATIONS BALANCE USED 6120 719998 SITE IMPROVEMENTS .00 .00 .00 732.00 -732.00 \*\*\* 6201 719998 BUILDING ALTERATIONS & IMPROV -22,451.95 287,949.55 1,017,490.11 \*\*\* .00 -1,305,439.66 6202 719998 DESIGN .00 7,453.60 10,115.60 79,953.40 -90,069.00 \*\*\* -23,250.00 6215 719998 SPECIALITY CONSULTING .00 -23,250.00 28,325.00 -5,075.00 \*\*\* 622201 719998 DSA INSPECTION -6,460.00 33,820.00 -33,820.00 \*\*\* .00 .00 TOTAL Capital Expenses .00 -44,708.35 274,815.15 1,160,320.51 \*\*\* -1,435,135.66 TOTAL ORGANIZATION 50200 BOND FUND CHABOT COLLEGE Expenditures TOTAL .00 -44,708.35 274,815.15 1,160,320.51 -1,435,135.66 NET .00 44,708.35 -274,815.15 -1,160,320.51 1,435,135.66 TOTAL FUND 562600 CAMPUS SECURITY TOTAL Expenditures .00 -44,708.35 274,815.15 1,160,320.51 -1,435,135.66

44,708.35

-274,815.15

-1,160,320.51

.00

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM PAGE: 22

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 562601 CAMPUSWIDE FA PA UPGRADE PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50200 BOND FUND CHABOT COLLEGE

ACCT P	ROG ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6215 71 622201 71	9998 BUILDING ALTERATIONS & IMPROV 9998 SPECIALITY CONSULTING 9998 DSA INSPECTION 9998 TESTS & INSPECTIONS	.00 .00 .00	1,525.00 12,825.00	40,574.37 4,575.00 12,825.00 .00	.00	-40,574.37 -10,675.00 -12,825.00 -20,000.00	* * * * * * * * *
TOTAL	Capital Expenses	.00	119,073.25	57,974.37	26,100.00	-84,074.37	***
TOTAL ORG	ANIZATION BOND FUND CHABOT COLLEGE						
TOTAL	Expenditures	.00	119,073.25	57,974.37	26,100.00	-84,074.37	***
NET		.00	-119,073.25	-57,974.37	-26,100.00	84,074.37	***
TOTAL FUN 562601	D CAMPUSWIDE FA PA UPGRADE						
TOTAL	Expenditures	.00	119,073.25	57,974.37	26,100.00	-84,074.37	***
NET		.00	-119,073.25	-57,974.37	-26,100.00	84,074.37	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 23

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 562602 CAMPUSWIDE LED LIGHTING PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50200 BOND FUND CHABOT COLLEGE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5711	719998	B LEGAL ADVERTISING	.00	323.68	323.68	.00	-323.68	***
TOTAL		Other Operating Expenses & Ser	.00	323.68	323.68	.00	-323.68	***
6215	719998	S SPECIALITY CONSULTING	. 00	25,000.00	25,000.00	13,550.00	-38,550.00	***
TOTAL		Capital Expenses	.00	25,000.00	25,000.00	13,550.00	-38,550.00	***
TOTAL ORGANIZATION 50200 BOND FUND CHABOT COLLEGE								
TOTAL		Expenditures	. 00	25,323.68	25,323.68	13,550.00	-38,873.68	***
NET			. 00	-25,323.68	-25,323.68	-13,550.00	38,873.68	***
TOTAL F	UND	CAMPUSWIDE LED LIGHTING						
TOTAL		Expenditures	.00	25,323.68	25,323.68	13,550.00	-38,873.68	***
NET			.00	-25,323.68	-25,323.68	-13,550.00	38,873.68	***

### Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 24

FINANCE MGR:

FUND:

COAS: 1 Chabot - Las Positas C C D

563700 LIBRARY, OFFICES, LABS, CLASSRMS B2100

PRED ORG: 5500 BOND FUND RESTRICTED

ORG: 50300 BOND FUND LAS POSITAS COLLEGE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
2303	719998	OVERTIME	.00	434.01	434.01	.00	-434.01	***
TOTAL		Classified Salaries	.00	434.01	434.01	.00	-434.01	***
3320 3520	719998	OASDHI OTHER CLASS EMPLOYEES SUI OTHER CLASS EMPLOYEES	.00			.00	-32.33 22	* * * * * *
3620	719998	WCI OTHER CLASS EMPLOYEES	.00	5.69	5.69	.00	-5.69	***
TOTAL		Fringe Benefits	.00	38.24	38.24	.00	-38.24	***
6202 6215 6222 6235 6241	719998 719998 719998	DESIGN SPECIALITY CONSULTING DSA PLAN CHECK CONSTRUCTION RENOVATION TESTS & INSPECTIONS	.00 .00 .00 .00	2,270.00 .00 .00	2,270.00 396,450.00 3,422.37	106,330.00 .00 94,125.05	-5,486,173.14 -108,600.00 -396,450.00 -97,547.42 -52,120.00	* * * * * * * * * * * *
TOTAL		Capital Expenses	.00	2,270.00	653,138.43	5,487,752.13	-6,140,890.56	***
TOTAL ORGANIZATION 50300 BOND FUND LAS POSITAS COLLEGE								
TOTAL TOTAL		Labor Expenditures	.00				-472.25 -6,140,890.56	* * * * * *
NET			.00	-2,742.25	-653,610.68	-5,487,752.13	6,141,362.81	***
TOTAL 563700		LIBRARY, OFFICES, LABS, CLASSRMS B2100						
TOTAL TOTAL		Labor Expenditures	.00				-472.25 -6,140,890.56	* * * * * *
NET			.00	-2,742.25	-653,610.68	-5,487,752.13	6,141,362.81	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 25

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 563701 AV UPGRADE B2420

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5711 71999	8 LEGAL ADVERTISING	.00	409.80	409.80	.00	-409.80	***
TOTAL	Other Operating Expenses & Ser	.00	409.80	409.80	.00	-409.80	***
6215 71999	8 DESIGN 8 SPECIALITY CONSULTING 8 DSA INSPECTION Capital Expenses	.00	1,228.35 .00 .00 1,228.35	.00	.00	-17,053.76 .00 -3,800.00 -20,853.76	* * * * * * * * *
TOTAL ORGANI 50300	ZATION BOND FUND LAS POSITAS COLLEGE						
TOTAL	Expenditures	.00	1,638.15	1,638.15	19,625.41	-21,263.56	***
NET		.00	-1,638.15	-1,638.15	-19,625.41	21,263.56	***
TOTAL FUND 563701	AV UPGRADE B2420						
TOTAL	Expenditures	.00	1,638.15	1,638.15	19,625.41	-21,263.56	***
NET		.00	-1,638.15	-1,638.15	-19,625.41	21,263.56	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 26

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 563715 PUBLIC SAFETY CTR & ADV MFG & TRANS

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6202 6215 6241	719998	DESIGN SPECIALITY CONSULTING TESTS & INSPECTIONS	.00	1,132.50	1,132.50	18,992.50	-3,553,551.35 -20,125.00 -43,900.00	* * * * * * * * *
TOTAL		Capital Expenses	.00	88,797.40	88,797.40	3,528,778.95	-3,617,576.35	***
TOTAL 6	ORGANIZ	ATION BOND FUND LAS POSITAS COLLEGE						
TOTAL		Expenditures	. 00	88,797.40	88,797.40	3,528,778.95	-3,617,576.35	***
NET			.00	-88,797.40	-88,797.40	-3,528,778.95	3,617,576.35	***
TOTAL : 563715		PUBLIC SAFETY CTR & ADV MFG & TRANS						
TOTAL		Expenditures	.00	88,797.40	88,797.40	3,528,778.95	-3,617,576.35	***
NET			.00	-88,797.40	-88,797.40	-3,528,778.95	3,617,576.35	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 27

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 563730 CAMPUS VEHICULAR CIRCULATION

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6215 719998	S SPECIALITY CONSULTING	.00	.00	.00	570.75	-570.75	***
TOTAL	Capital Expenses	.00	.00	.00	570.75	-570.75	***
TOTAL ORGANIZ 50300 TOTAL	ZATION BOND FUND LAS POSITAS COLLEGE Expenditures	. 00	.00	.00	570.75	-570.75	***
NET		.00	.00	.00	-570.75	570.75	***
TOTAL FUND 563730	CAMPUS VEHICULAR CIRCULATION						
TOTAL	Expenditures	.00	.00	.00	570.75	-570.75	***
NET		.00	.00	.00	-570.75	570.75	***

Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019 RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 28

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 563740 ATHLETIC FIELDS

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6215 719998	3 SPECIALITY CONSULTING	.00	.00	2,985.00	.00	-2,985.00	***
TOTAL	Capital Expenses	.00	.00	2,985.00	.00	-2,985.00	***
TOTAL ORGANIZ 50300	ZATION BOND FUND LAS POSITAS COLLEGE						
TOTAL	Expenditures	.00	.00	2,985.00	.00	-2,985.00	***
NET		.00	.00	-2,985.00	.00	2,985.00	***
TOTAL FUND 563740	ATHLETIC FIELDS						
TOTAL	Expenditures	.00	.00	2,985.00	.00	-2,985.00	***
NET		.00	.00	-2,985.00	.00	2,985.00	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 29

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 563741 SOCCER FIELD REPLACEMENT PROJ

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6202	719998	SITE IMPROVEMENTS DESIGN TESTS & INSPECTIONS	.00 .00	1,900.00	1,900.00		-1,107,500.00 -17,400.00 -4,425.00	* * * * * *
TOTAL		Capital Expenses	.00	1,900.00	1,900.00	1,127,425.00	-1,129,325.00	***
TOTAL O	RGANIZ	ATION BOND FUND LAS POSITAS COLLEGE						
TOTAL		Expenditures	.00	1,900.00	1,900.00	1,127,425.00	-1,129,325.00	***
NET			.00	-1,900.00	-1,900.00	-1,127,425.00	1,129,325.00	***
TOTAL F 563741	UND	SOCCER FIELD REPLACEMENT PROJ						
TOTAL		Expenditures	.00	1,900.00	1,900.00	1,127,425.00	-1,129,325.00	***
NET			.00	-1,900.00	-1,900.00	-1,127,425.00	1,129,325.00	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 30

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 563810 AGRICULTURAL SCIENCES-HOLTICULTURE

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6202 6215 6241	719998	DESIGN SPECIALITY CONSULTING TESTS & INSPECTIONS	.00	0 1,035.00	1,035.00	39,257.00	-433,400.00 -40,292.00 -5,000.00	* * * * * * * * *
TOTAL		Capital Expenses	.0	0 17,791.80	17,791.80	460,900.20	-478,692.00	***
TOTAL 50300	ORGANIZ	ATION BOND FUND LAS POSITAS COLLEGE						
TOTAL		Expenditures	.0	0 17,791.80	17,791.80	460,900.20	-478,692.00	***
NET			. 0	0 -17,791.80	-17,791.80	-460,900.20	478,692.00	***
TOTAL 563810		AGRICULTURAL SCIENCES-HOLTICULTURE						
TOTAL		Expenditures	.0	0 17,791.80	17,791.80	460,900.20	-478,692.00	***
NET			.0	0 -17,791.80	-17,791.80	-460,900.20	478,692.00	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 31

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 563811 AGRICULTURAL SCIENCES-VITICULTURE

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT PRO	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5884 7199	8 BUSINESS EXPENSE	.00	272.91	272.91	.00	-272.91	***
TOTAL	Other Operating Expenses & Ser	.00	272.91	272.91	.00	-272.91	***
6241 7199	8 TESTS & INSPECTIONS	.00	.00	.00	25,133.00	-25,133.00	***
TOTAL	Capital Expenses	.00	.00	.00	25,133.00	-25,133.00	***
TOTAL ORGAN 50300	BOND FUND LAS POSITAS COLLEGE						
TOTAL	Expenditures	.00	272.91	272.91	25,133.00	-25,405.91	***
NET		.00	-272.91	-272.91	-25,133.00	25,405.91	***
TOTAL FUND 563811	AGRICULTURAL SCIENCES-VITICULTURE						
TOTAL	Expenditures	.00	272.91	272.91	25,133.00	-25,405.91	***
NET		.00	-272.91	-272.91	-25,133.00	25,405.91	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM PAGE: 32

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 563830 CLASSROOM/LAB EQUIP & LIBRARY MAT'L

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
4320 719998	PROGRAM/OPERATING SUPPLIES	.00	.00	373.31	.00	-373.31	***
TOTAL	Supplies Expense	.00	.00	373.31	.00	-373.31	***
6401 719998 640101 719998	B LIBRARY BOOKS B EQUIPMENT <\$1000 B EQUIPMENT \$1000 to 4999.99 B EQUIPMENT >\$5000 CAPITALIZED Capital Expenses	.00	.00 8,614.36 67,735.00	21,512.01 36,316.95 423.69 67,735.00 125,987.65	135,431.06 4,735.73	-321,415.19 -171,748.01 -5,159.42 -73,352.52 -571,675.14	*** *** ***
TOTAL ORGANIZ 50300	ATION BOND FUND LAS POSITAS COLLEGE						
TOTAL	Expenditures	.00	85,592.98	126,360.96	445,687.49	-572,048.45	***
NET		.00	-85,592.98	-126,360.96	-445,687.49	572,048.45	***
TOTAL FUND 563830	CLASSROOM/LAB EQUIP & LIBRARY MAT'L						
TOTAL	Expenditures	.00	85,592.98	126,360.96	445,687.49	-572,048.45	***
NET		.00	-85,592.98	-126,360.96	-445,687.49	572,048.45	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM PAGE: 33

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND:

563860 LPC PROJECT & CONSTRUCTION MGMNT

PRED ORG: 5500 BOND FUND RESTRICTED

BOND FUND LAS POSITAS COLLEGE ORG: 50300

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
2111	719998	MANAGEMENT	159,070.00	13,255.83	39,767.49	.00	119,302.51	25
TOTAL		Classified Salaries	159,070.00	13,255.83	39,767.49	.00	119,302.51	25
3221 3321 3421 3521 3621	719998 719998 719998	PERS-CLASS ADMINISTRATORS OASDHI CLASS MANAGERS H & W CLASS MANAGERS SUI CLASS MANAGERS WCI CLASS MANAGERS	31,369.00 10,547.00 20,920.00 80.00 2,100.00	2,614.18 994.18 858.88 6.63 173.48	7,842.54 2,982.52 2,576.64 19.89 520.44	.00	23,526.46 7,564.48 18,343.36 60.11	25 28 12 25
TOTAL	, 22230	Fringe Benefits	65,016.00	4,647.35		.00	1,579.56 51,073.97	25 21
4301	719998	OFFICE SUPPLIES	.00	542.88	696.38	927.93	-1,624.31	***
TOTAL		Supplies Expense	.00	542.88	696.38	927.93	-1,624.31	***
5610 5647		RENTAL OF EQUIPMENT EQUIP MAINT - ALL OTHER SERVIC	.00	.00	.00 27.50	4,505.38 2,635.94	-4,505.38 -2,663.44	* * * * * *
TOTAL		Other Operating Expenses & Ser	.00	.00	27.50	7,141.32	-7,168.82	***
6210 6215 6235 TOTAL	719998	CONSTRUCTION MANAGEMENT SPECIALITY CONSULTING CONSTRUCTION RENOVATION Capital Expenses	.00 .00 .00	44,966.25 .00 .00 44,966.25	76,615.00 .00 .00 76,615.00	450.00 131,413.00	-2,288,551.00 -450.00 -131,413.00 -2,420,414.00	* * * * * * * * *
TOTAL 50300	ORGANIZ	ATION BOND FUND LAS POSITAS COLLEGE						
TOTAL TOTAL		Labor Expenditures	224,086.00	17,903.18 45,509.13	53,709.52 77,338.88		170,376.48 -2,429,207.13	24 ***
NET			-224,086.00	-63,412.31	-131,048.40	-2,351,868.25	2,258,830.65	1108

Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 34

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND:

563860 LPC PROJECT & CONSTRUCTION MGMNT

PRED ORG: 5500 BOND FUND RESTRICTED

50300 BOND FUND LAS POSITAS COLLEGE ORG:

ACCT PI	ROG ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
TOTAL FUNI 563860	D LPC PROJECT & CONSTRUCTION MGMNT						
TOTAL TOTAL	Labor Expenditures	224,086.00 .00	17,903.18 45,509.13	• • • • • • • • • • • • • • • • • • • •	.00 2,351,868.25	170,376.48 -2,429,207.13	24 ***
NET		-224,086.00	-63,412.31	-131,048.40	-2,351,868.25	2,258,830.65	1108

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 35

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 563900 CAMPUS SECURITY

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5110	719998	PROFESSIONAL SERVICES	.00	.00	.00	11,683.00	-11,683.00	***
5641		MAINTENANCE - SOFTWARE	.00	.00	1,123.01		-1,123.01	***
5711	719998	LEGAL ADVERTISING	.00	323.68	323.68	.00	-323.68	***
TOTAL		Other Operating Expenses & Ser	.00	323.68	1,446.69	11,683.00	-13,129.69	***
6201	719998	BUILDING ALTERATIONS & IMPROV	.00	53,795.00	188,282.50	25,628.00	-213,910.50	***
6202	719998	DESIGN	.00	7,453.60	10,115.60		-90,069.00	***
6215	719998	SPECIALITY CONSULTING	.00	.00	.00	17,650.00	-17,650.00	***
TOTAL		Capital Expenses	.00	61,248.60	198,398.10	123,231.40	-321,629.50	***
TOTAL 50300	ORGANIZ	ATION BOND FUND LAS POSITAS COLLEGE						
TOTAL		Expenditures	.00	61,572.28	199,844.79	134,914.40	-334,759.19	***
NET			.00	-61,572.28	-199,844.79	-134,914.40	334,759.19	***
TOTAL 563900	FUND	CAMPUS SECURITY						
TOTAL		Expenditures	.00	61,572.28	199,844.79	134,914.40	-334,759.19	***
NET			.00	-61,572.28	-199,844.79	-134,914.40	334,759.19	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:09 PM PAGE: 36

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 563920 EIR SERVICES

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6120 719998	B SITE IMPROVEMENTS	.00	.00	.00	978.25	-978.25	***
TOTAL	Capital Expenses	.00	.00	.00	978.25	-978.25	***
TOTAL ORGANIZ	ZATION BOND FUND DISTRICT-WIDE						
TOTAL	Expenditures	.00	.00	.00	978.25	-978.25	***
NET		.00	.00	.00	-978.25	978.25	***
TOTAL FUND 563920	EIR SERVICES						
TOTAL	Expenditures	.00	.00	.00	978.25	-978.25	***
NET		.00	.00	.00	-978.25	978.25	***

Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

\* \* \* REPORT CONTROL INFORMATION \* \* \*

RUN DATE: 10/17/2019 TIME: 12:09 PM

PAGE: 37

PARAMETER SEQUENCE NUMBER: 78348

FISCAL YEAR: 20

CHART OF ACCOUNTS: 1
AS OF DATE: 30-SEP-2019

PRINT TOTALS: Y
PRINT NET TOTALS: Y
FROM FUND: 561%
TO FUND: 569999
FROM ORGN PRED:
TO ORGN PRED:
FROM ORGN:
TO ORGN:

ACCURAL INCLUDED: N

NUMBER OF PRINTED LINES PER PAGE: 55

RECORD COUNT: 180



# Facilities Modernization Program Funded by Measure B Data Date: September 30, 2019

		(A)	(B)	(C)	(D)
Fund	Fund Description	Current Budget	Actual Expenditures to Date	Unpaid Commitments	Remaining Budget A - (B+C) = D
DISTRICTWIDE TOT	ALS	90,621,191	90,104,665	51,862	464,664
CHABOT COLLEGE	TOTALS	264,146,752	247,262,356	12,466,767	4,417,629
LAS POSITAS COLLE	EGE TOTALS	248,455,295	249,893,254	5,842	(1,443,800)
PROGRAM TOTALS		603,223,238	587,260,275	12,524,471	3,438,492



# Facilities Modernization Program Funded by Measure B Data Date: September 30, 2019

	(A)	(B)	(C)	(D)
Fund Description	Current Budget	Actual Expenditures to Date	Unpaid Commitments	Remaining Budget A - (B+C) = D
VIDE				
Information Technology & Tech Upgrades (B,N,R)	11,046,068	11,046,068	-	-
Classroom, Lab Equipment, Chabot College (N)	10,027,359	10,026,815	-	544
Classroom, Lab Equipment, Las Positas College (R)	8,017,950	8,017,950	-	-
District ITS Data Center Upgrade (B)	17,269	17,269	-	-
Sungard Enrollment Management Suite (B,N,R)	675,728	675,728	-	-
IBM Enterprise Server-Sungard Banner System (B,N,R)	472,724	472,724	-	-
Enterprise ERP Hardware/Software (E,N,R)	1,923,734	1,923,734	-	-
New Buildings IT (B,N,R)	-	-	-	-
On-Going Maint & Repairs: Roofs, HVAC (A,B,C,E)	8,407,075	8,370,929	10,250	25,896
Mitigation Property Clean Up (E)	35,275	35,275	-	-
M&O Equipment (B,N,R)	1,470,801	1,470,801	-	-
Warehouse Services (F,O)	19,390	19,390	-	-
Campus Security Equipment (B,N,R)	194,260	194,260	-	-
Program Level Services, District (A,B,C,D,E)	13,219,845	12,990,478	41,612	187,754
Dublin Education Center (E)	9,963,932	9,963,932	-	-
Dublin Education Center Phase II (E)	188,580	188,580	-	-
Dublin Education Center Phase III (E)	7,598,174	7,598,174	-	-
Union City Education Center (E)	97,329	97,329	-	-
Site Improvements (E,F,O)	112,248	112,248	-	-
Districtwide Multi-Function Copier Equipment (B,N,R)	803,135	803,135	-	-
Energy Projects (K,V)	4,125,160	3,956,096	-	169,063
Photov oltaic Solar Project, LPC (V)	5,505,981	5,505,981	-	-
	Information Technology & Tech Upgrades (B,N,R)  Classroom, Lab Equipment, Chabot College (N)  Classroom, Lab Equipment, Las Positas College (R)  District ITS Data Center Upgrade (B)  Sungard Enrollment Management Suite (B,N,R)  IBM Enterprise Serv er-Sungard Banner System (B,N,R)  Enterprise ERP Hardware/Software (E,N,R)  New Buildings IT (B,N,R)  On-Going Maint & Repairs: Roofs, HVAC (A,B,C,E)  Mitigation Property Clean Up (E)  M&O Equipment (B,N,R)  Warehouse Services (F,O)  Campus Security Equipment (B,N,R)  Program Level Services, District (A,B,C,D,E)  Dublin Education Center (E)  Dublin Education Center Phase III (E)  Union City Education Center (E)  Site Improvements (E,F,O)  Districtwide Multi-Function Copier Equipment (B,N,R)  Energy Projects (K,V)	Fund Description  WIDE  Information Technology & Tech Upgrades (B,N,R) 11,046,068 Classroom, Lab Equipment, Chabot College (N) 10,027,359 Classroom, Lab Equipment, Las Positas College (R) 8,017,950 District ITS Data Center Upgrade (B) 17,269 Sungard Enrollment Management Suite (B,N,R) 675,728 IBM Enterprise Server-Sungard Banner System (B,N,R) 472,724 Enterprise ERP Hardware/Software (E,N,R) 1,923,734 New Buildings IT (B,N,R) - On-Going Maint & Repairs: Roofs, HVAC (A,B,C,E) 8,407,075 Mitigation Property Clean Up (E) 35,275 M&O Equipment (B,N,R) 1,470,801 Warehouse Services (F,O) 19,390 Campus Security Equipment (B,N,R) 194,260 Program Level Services, District (A,B,C,D,E) 13,219,845 Dublin Education Center (E) 9,963,932 Dublin Education Center Phase III (E) 7,598,174 Union City Education Center (E) 97,329 Site Improvements (E,F,O) 112,248 Districtwide Multi-Function Copier Equipment (B,N,R) 803,135 Energy Projects (K,V) 4,125,160	Fund Description	Fund Description   Pund Descri



# Facilities Modernization Program Funded by Measure B Data Date: September 30, 2019

		(A)	(B)	(C)	(D)
Fund	Fund Description	Current Budget	Actual Expenditures to Date	Unpaid Commitments	Remaining Budget A - (B+C) = D
551062	Prop 39 Energy Improvements, Year 1 (K,V)	703,896	703,896	-	-
551063	Prop 39 Energy Improvements, Year 2 (K,V)	444,577	444,577	-	-
551064	Prop 39 Energy Improvements, Year 3 (K,V)	9,461	-	-	9,461
551065	Prop 39 Energy Improvements, Year 4 (K,V)	8,720	-	-	8,720
551066	Prop 39 Energy Improvements, Year 5 (K,V)	-	35,727	-	(35,727)
551068	Flow Battery, LPC (V)	500,000	498,639	-	1,361
551070	Property Acquisition - Inman (E)	409,633	409,633	-	-
551080	District Office Debt Service (E)	4,194,530	4,096,938	-	97,592
551090	Facilities Master Plan Update (E)	428,358	428,358	-	-
551100	District Contingency Fund		-	-	-
DISTRICTW	VIDE TOTALS	90,621,191	90,104,665	51,862	464,664



552480

Community and Student Services Center \* (E,F,I)

## **Chabot-Las Positas Community College District**

## Facilities Modernization Program Funded by Measure B Data Date: September 30, 2019

Project Budget Summary

		(A)	(B)	(C)	(D)
Fund	Fund Description	Current Budget	Actual Expenditures to Date	Unpaid Commitments	Remaining Budget A - (B+C) = D
CHABOT (	COLLEGE				
552110	Library Building - 100 w/Seismic Strengthening (F,M)	5,921,664	5,921,664	-	-
552111	B100 TV Studio (F)	125,660	125,660	-	-
552112	Library Elevator & Interiors - 100 (F)	1,551,284	1,551,284	-	-
552120	Administration Building - 200 (E,K,N,Y)	856,101	856,101	-	-
552130	Classroom Buildings 300, 500 (E,F)	10,740,754	10,740,754	-	-
552170	Instructional Office Building 400 (H)	18,351,668	18,351,668	-	-
552180	Classroom Buildings 800, 900, 1000 (E,F)	5,023,788	5,023,788	-	-
552200	Art Classrooms & Studios, Bldg 1000 (E,F)	249,174	249,174	-	-
552210	Buildings - 1100, 1500, 2000 (F)	20,966	20,966	-	0
552220	Buildings - 1200, 1300, PAC Plaza (E,F,N)	11,198,654	11,198,654	-	-
552240	Industrial Technology Buildings - 1400, 1600 (E,F)	6,006,082	6,006,082	-	-
552260	Engineering Building - 1600 (F)	35,877	35,877	-	-
552280	Classroom Bldgs 1700, 1800 (E,F)	8,252,567	8,252,567	-	-
552290	Science Lecture Hall / Planetarium - 1900 (F)	3,264,445	3,264,445	-	-
552310	Biological Classrooms & Labs - 2100 (F)	471,463	471,463	-	-
552315	Biology Building Phase I - 2100 (F)	26,950,000	12,041,436	12,039,211	2,869,353
552320	Health Science Building - 2200 (E,F)	2,870,102	2,870,102	-	-
552330	Student Union/Cafeteria Building - 2300 (E,F,Y)	985,008	985,008	-	-
552430	Building 3400, Automotive Technology (E,F)	1,804,307	1,804,307	-	-
552440	Building 3500, Early Childhood Center (E,F)	110,599	110,599	-	-
552460	Building 3800 Bookstore / Energy (J)	4,299,763	4,299,763	-	-

37,095,817

37,095,817



**CHABOT COLLEGE TOTALS** 

## **Chabot-Las Positas Community College District**

## Facilities Modernization Program Funded by Measure B Data Date: September 30, 2019

Project Budget Summary

(D) (C) (A) (B) Actual **Expenditures** Remaining Budget Current Unpaid **Fund Fund Description Budget** to Date Commitments A - (B+C) = D552481 Chabot Hesperian Landscape (F) 1,099,511 1,099,511 552490 Physical Education Complex Buildings (F) 22,859,981 22,859,981 552491 PE Complex - Strength & Fitness Center, Bldg 4000 (F) 6,088,167 6,088,167 552492 Fire Technology - 2900 (F) 12,136 12,136 552500 Athletic Fields / Tennis Courts (E,F) 7,104,697 7,104,697 Grand Court (F) 552510 15,394 15,394 552520 Campus Repairs / Small Projects (E,F) 3,295,560 2,631,282 363,057 301,221 552521 Water Charging Stations (E,F) 47,298 47,298 552530 Temporary Faculty Offices (F) 1,466,208 1,466,208 552540 Classroom/Lab Equipment & Library Materials (F) 12,397,998 12,397,998 552560 CC Project & Construction Management (Y) 5,064,367 5,064,367 (0)552590 Central Plant (Mech Conv Def Bldgs/IT Infrastructure) (F 26,307,517 26,307,517 552620 Parking Lots A & B and G & H (F) 9,438,716 9,438,716 552621 Soccer Field Improvements (F) 977,743 977,743 552622 632,063 Parking Lot Security and Marguee (F) 632,063 552630 Maintenance & Operations Facility (H) 224,445 224,445 552640 Swimming Pool (E,F) 3,386,335 2,074,781 64,500 1,247,054 552650 Miscellaneous Site Work / Campus Security (F) 2,351,037 2,351,037 552651 Campus Signage (F) 573,457 573,457 552660 Photo Voltaic Project (K) 12,034,663 12,034,663 552670 Seismic Upgrades (F) 2,583,716 2,583,716 552680 Sustainability (F)

264,146,752

247,262,356

12,466,767

4,417,629



# Facilities Modernization Program Funded by Measure B Data Date: September 30, 2019

		(A)	(B)	(C)	(D)
Fund	Fund Description	Current Budget	Actual Expenditures to Date	Unpaid Commitments	Remaining Budget A - (B+C) = D
LAS POSI	TAS COLLEGE				
553700	Multi-Disciplinary Education Building (E,O,S)	6,645,953	6,645,953	-	-
553705	Multi-Disciplinary Education Building - Repairs (E,O,S)	922,039	922,039	-	-
553710	Child Development Center (E,O,S)	13,955,110	13,955,110	-	-
553720	College Center for Arts (E,O)	46,514,878	46,514,878	-	-
553730	Science & Technology (E,O,S,T)	15,228,489	15,228,489	-	-
553740	PE Complex (GYM) (E,O)	1,431,365	1,431,365	-	-
553745	PE Complex (GYM) - Repairs (E,O)	417,467	417,467	-	-
553750	Student Services & Central Administration (O,P,U,X)	34,500,916	34,500,916	-	-
553751	Buildings - 500, 600, 700, 1700 Renovations (E,O)	3,716,321	3,716,321	-	-
553752	Buildings 100,700,900,1300,1700 Renovations/Repurpos	1,320,550	1,320,550	-	-
553753	ADA Upgrade (O, E)	459,298	459,298	-	-
553770	Renovations (E,O)	1,102,163	1,102,163	-	-
553771	Small Projects/Scheduled Maintenance (E,O)	2,414,416	2,414,416	-	-
553772	Amphitheater Surface Issue (E,O)	311,252	311,252	-	-
553780	Library, Building 2000 Remodel (E,O,R,U)	4,742,507	4,742,507	-	-
553790	Maintenance and Operations Facility (E,O)	7,915,466	7,915,466	-	-
553800	Building 100A-Construction (O,P,U)	218,670	218,670	-	-
553805	New B100, Academic Building, FPP (O,P,U)	24,861,215	26,458,863	575	(1,598,223)
553806	Building 700 Renovation (O,P,U)	2,067,927	2,067,927	-	-
553807	Temporary Relocatable Project (O,P,U)	866,296	866,296	-	-
553810	Campus Repairs (Exterior Paint & Fencing) (O)	119,241	119,241	-	-
553820	Parking Lot #6 (X,P)	994,074	994,074	-	-




# Facilities Modernization Program Funded by Measure B Data Date: September 30, 2019

		(A)	(B)	(C)	(D)
Fund	Fund Description	Current Budget	Actual Expenditures to Date	Unpaid Commitments	Remaining Budget A - (B+C) = D
553830	LPC Instructional Equipment (O)	4,641,721	4,641,721	-	-
553840	Central Utility Plant (O,V)	11,651,832	11,651,832	-	-
553850	Districtwide Information Technology Building (E,O,W)	6,869,220	6,869,220	-	-
553860	LPC Program & Construction Management (Y)	7,547,528	7,323,909	-	223,619
553870	Campus Entry Enhancements (P,X)	100,553	100,553	-	-
553880	Campus Boulev ard Phases I-III (P,X)	2,635,951	2,635,951	-	-
553900	PE Phase III/Collier Creek (Outside Loop Road) (E,O)	9,619,977	9,619,977	-	-
553910	Aquatic Center & Soccer Fields (E,O)	13,530,443	13,530,443	-	-
553920	EIR Services (Y)	4,675,967	4,739,896	5,267	(69,196)
553930	Utilities Infrastructure Upgrade (V,X)	586,092	586,092	-	-
553940	Parking Lot H & Solar PV System (V)	13,253,341	13,253,341	-	-
553950	Fire Alarm/Security Upgrade (O)	2,617,059	2,617,059	-	-
LAS POSITA	AS COLLEGE TOTALS	248,455,295	249,893,254	5,842	(1,443,800)



# Chabot-Las Positas Community College District Facilities Modernization Program Funded by Measure B Data Date: September 30, 2019



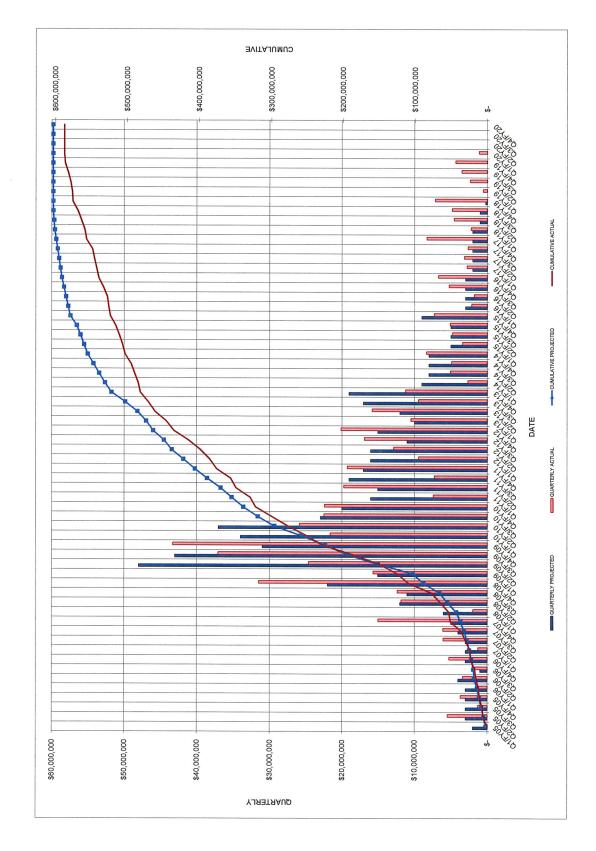

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 1

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 551020 Major Maintenance & Repairs

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6215 719999	9 SPECIALITY CONSULTING	.00	.00	.00	11,900.00	-11,900.00	***
TOTAL	Capital Expenses	.00	.00	.00	11,900.00	-11,900.00	***
TOTAL ORGANIZ 50100	ZATION BOND FUND DISTRICT-WIDE						
TOTAL	Expenditures	.00	.00	.00	11,900.00	-11,900.00	***
NET		.00	.00	.00	-11,900.00	11,900.00	***
TOTAL FUND 551020	Major Maintenance & Repairs						
TOTAL	Expenditures	.00	.00	.00	11,900.00	-11,900.00	***
NET		.00	.00	.00	-11,900.00	11,900.00	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 2

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 551030 Program Level Services District

PRED ORG: 5500 BOND FUND RESTRICTED
ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED	
5110 5701	719999 719999	PROFESSIONAL SERVICES ANNUAL FISCAL AUDIT	.0	•	,	•	-44,462.00 -9,450.00	* * * * * *	
TOTAL		Other Operating Expenses & Ser	.0	0 13,350.00	13,350.00	40,562.00	-53,912.00	***	
TOTAL ORGANIZATION 50100 BOND FUND DISTRICT-WIDE									
TOTAL		Expenditures	. 0	0 13,350.00	13,350.00	40,562.00	-53,912.00	***	
NET			.0	0 -13,350.00	-13,350.00	-40,562.00	53,912.00	***	
TOTAL F 551030	FUND	Program Level Services District							
TOTAL		Expenditures	.0	0 13,350.00	13,350.00	40,562.00	-53,912.00	***	
NET			.0	0 -13,350.00	-13,350.00	-40,562.00	53,912.00	***	

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 3

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 551068 FLOW BATTERY LPC (V) PRED ORG: 5500 BOND FUND RESTRICTED

ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6120 71999	9 SITE IMPROVEMENTS	.00	9,243.15	9,243.15	.00	-9,243.15	***
TOTAL	Capital Expenses	.00	9,243.15	9,243.15	.00	-9,243.15	***
TOTAL ORGANIZATION 50100 BOND FUND DISTRICT-WIDE							
TOTAL	Expenditures	.00	9,243.15	9,243.15	.00	-9,243.15	***
NET		.00	-9,243.15	-9,243.15	.00	9,243.15	***
TOTAL FUND 551068	FLOW BATTERY LPC (V)						
TOTAL	Expenditures	.00	9,243.15	9,243.15	.00	-9,243.15	***
NET		.00	-9,243.15	-9,243.15	.00	9,243.15	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 4

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 551080 District Office Debt Service

PRED ORG: 5500 BOND FUND RESTRICTED ORG: 50100 BOND FUND DISTRICT-WIDE

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
8910 89000	0 PROCEEDS OF GEN FIXED ASSETS	.00	19,383.99	58,151.97	.00	-58,151.97	***
TOTAL	Other Revenues	.00	19,383.99	58,151.97	.00	-58,151.97	***
TOTAL ORGANI 50100	ZATION BOND FUND DISTRICT-WIDE						
TOTAL	Revenues	.00	19,383.99	58,151.97	.00	-58,151.97	***
NET		.00	19,383.99	58,151.97	.00	-58,151.97	***
TOTAL FUND 551080	District Office Debt Service						
TOTAL	Revenues	.00	19,383.99	58,151.97	.00	-58,151.97	***
NET		.00	19,383.99	58,151.97	.00	-58,151.97	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 5

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 552315 NEW BIOLOGY RENOV - 2100 (F)

PRED ORG: 5500 BOND FUND RESTRICTED
ORG: 50200 BOND FUND CHABOT COLLEGE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6210 6215 622201 6235	719999 719999 719999 719999	DESIGN CONSTRUCTION MANAGEMENT SPECIALITY CONSULTING DSA INSPECTION CONSTRUCTION RENOVATION TESTS & INSPECTIONS	.00 .00 .00 .00	31,392.75 5,209.20 19,380.00 870,711.20	.00 36,100.00	313,882.05 47,891.80 169,325.00 11,406,657.20	-149,543.74 -373,191.30 -47,891.80 -205,425.00 -12,277,368.40 -15,748.47	* * * * * * * * * * * * * * *
TOTAL		Capital Expenses	.00	934,432.96	989,580.45	12,079,588.26	-13,069,168.71	***
TOTAL O	RGANIZ.	ATION BOND FUND CHABOT COLLEGE Expenditures	. 00	934,432.96	989,580.45	12,079,588.26	-13,069,168.71	***
NET			.00	-934,432.96	-989,580.45	-12,079,588.26	13,069,168.71	***
TOTAL F 552315	UND	NEW BIOLOGY RENOV - 2100 (F)						
TOTAL		Expenditures	.00	934,432.96	989,580.45	12,079,588.26	-13,069,168.71	***
NET			.00	-934,432.96	-989,580.45	-12,079,588.26	13,069,168.71	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 6

FINANCE MGR:

Chabot - Las Positas C C D COAS: 1

FUND:

552520 Campus Repairs 5500 BOND FUND RESTRICTED PRED ORG: ORG: 50200 BOND FUND CHABOT COLLEGE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5110 5647		PROFESSIONAL SERVICES EQUIP MAINT - ALL OTHER SERVIC	.00	•	· ·		-12,000.00 -10,957.00	* * * * * *
TOTAL		Other Operating Expenses & Ser	.00	12,000.00	12,000.00	10,957.00	-22,957.00	***
	719999 719999	DESIGN EQUIPMENT <\$1000 CQUIPMENT \$1000 to 4999.99 EQUIPMENT >\$5000 CAPITALIZED	.00 .00 .00	115,863.42 .00	115,863.42 .00	.00 2,053.44	-94,706.25 -115,863.42 -2,053.44 -288,643.78	* * * * * * * * *
TOTAL		Capital Expenses	.00	149,167.38	149,167.38	352,099.51	-501,266.89	***
TOTAL (	ORGANIZ	ATION BOND FUND CHABOT COLLEGE						
TOTAL		Expenditures	.00	161,167.38	161,167.38	363,056.51	-524,223.89	***
NET			.00	-161,167.38	-161,167.38	-363,056.51	524,223.89	***
TOTAL 1 552520		Campus Repairs						
TOTAL		Expenditures	.00	161,167.38	161,167.38	363,056.51	-524,223.89	***
NET			.00	-161,167.38	-161,167.38	-363,056.51	524,223.89	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 7

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D FUND: 552560 CC Project & Construction Mgmt

PRED ORG: 5500 BOND FUND RESTRICTED
ORG: 50200 BOND FUND CHABOT COLLEGE

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
588402 719999	MOVING/RELOCATION EXPENSE	.00	.00	.00	7,690.72	-7,690.72	***
TOTAL	Other Operating Expenses & Ser	.00	.00	.00	7,690.72	-7,690.72	***
TOTAL ORGANIZ 50200	ZATION BOND FUND CHABOT COLLEGE						
TOTAL	Expenditures	.00	.00	.00	7,690.72	-7,690.72	***
NET		.00	.00	.00	-7,690.72	7,690.72	***
TOTAL FUND 552560	CC Project & Construction Mgmt						
TOTAL	Expenditures	.00	.00	.00	7,690.72	-7,690.72	***
NET		.00	.00	.00	-7,690.72	7,690.72	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 8

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 552640 Swimming Pool

PRED ORG: 5500 BOND FUND RESTRICTED
ORG: 50200 BOND FUND CHABOT COLLEGE

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
5611	719999	RENTAL OF FACILITIES	.00	.00	.00	15,000.00	-15,000.00	***
TOTAL		Other Operating Expenses & Ser	.00	.00	.00	15,000.00	-15,000.00	***
6120 6222		SITE IMPROVEMENTS DSA PLAN CHECK	.00		.00 535.00	49,500.00	-49,500.00 -535.00	* * * * * *
TOTAL		Capital Expenses	.00	535.00	535.00	49,500.00	-50,035.00	***
TOTAL 50200	ORGANIZ	ATION BOND FUND CHABOT COLLEGE						
TOTAL		Expenditures	.00	535.00	535.00	64,500.00	-65,035.00	***
NET			.00	-535.00	-535.00	-64,500.00	65,035.00	***
TOTAL 552640	FUND	Swimming Pool						
TOTAL		Expenditures	.00	535.00	535.00	64,500.00	-65,035.00	***
NET			.00	-535.00	-535.00	-64,500.00	65,035.00	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 9

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 553750 Student Services & Central Admin

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6235 719999	O CONSTRUCTION RENOVATION	.00	.00	-1,333.20	1,333.20	.00	***
TOTAL	Capital Expenses	.00	.00	-1,333.20	1,333.20	.00	***
TOTAL ORGANIZ 50300	ZATION BOND FUND LAS POSITAS COLLEGE						
TOTAL	Expenditures	.00	.00	-1,333.20	1,333.20	.00	***
NET		.00	.00	1,333.20	-1,333.20	.00	***
TOTAL FUND 553750	Student Services & Central Admin						
TOTAL	Expenditures	.00	.00	-1,333.20	1,333.20	.00	***
NET		.00	.00	1,333.20	-1,333.20	.00	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 10

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 553805 New B100 Academic Building FPP

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT	PROG	ACCOUNT TITLE	ADJUSTED BUDGET		CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6235 6241	719999 719999	CONSTRUCTION RENOVATION TESTS & INSPECTIONS		00 00	996,491.75 .00	14,612.53 .00	.00 575.25	-14,612.53 -575.25	* * * * * *
TOTAL		Capital Expenses	. (	00	996,491.75	14,612.53	575.25	-15,187.78	***
TOTAL 6	ORGANIZ	ATION BOND FUND LAS POSITAS COLLEGE							
TOTAL		Expenditures	. (	00	996,491.75	14,612.53	575.25	-15,187.78	***
NET			. (	00	-996,491.75	-14,612.53	-575.25	15,187.78	***
TOTAL : 553805	FUND	New B100 Academic Building FPP							
TOTAL		Expenditures	. (	00	996,491.75	14,612.53	575.25	-15,187.78	***
NET			. (	00	-996,491.75	-14,612.53	-575.25	15,187.78	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 11

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 553860 LPC Program & Construction Mgmt

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
620203 719999	DESIGN REPROGRAPHICS	.00	.00	1,432.70	.00	-1,432.70	***
TOTAL	Capital Expenses	.00	.00	1,432.70	.00	-1,432.70	***
TOTAL ORGANIZ	ZATION BOND FUND LAS POSITAS COLLEGE Expenditures	.00	.00	1,432.70	.00	-1,432.70	***
NET		.00	.00	-1,432.70	.00	1,432.70	***
TOTAL FUND 553860	LPC Program & Construction Mgmt			=, ===		2, 3321.13	
TOTAL	Expenditures	.00	.00	1,432.70	.00	-1,432.70	***
NET		.00	.00	-1,432.70	.00	1,432.70	***

## Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 12

FINANCE MGR:

COAS: 1 Chabot - Las Positas C C D

FUND: 553920 EIR Services

PRED ORG: 5500 BOND FUND RESTRICTED

ACCT PROG	ACCOUNT TITLE	ADJUSTED BUDGET	CURRENT PERIOD ACTIVITY	YEAR TO DATE ACTIVITY	BUDGET RESERVATIONS	AVAILABLE BALANCE	% BGT USED
6120 719999	SITE IMPROVEMENTS	.00	.00	.00	5,267.01	-5,267.01	***
TOTAL	Capital Expenses	.00	.00	.00	5,267.01	-5,267.01	***
TOTAL ORGANIZ 50300	ATION BOND FUND LAS POSITAS COLLEGE						
TOTAL	Expenditures	.00	.00	.00	5,267.01	-5,267.01	***
NET		.00	.00	.00	-5,267.01	5,267.01	***
TOTAL FUND 553920	EIR Services						
TOTAL	Expenditures	.00	.00	.00	5,267.01	-5,267.01	***
NET		.00	.00	.00	-5,267.01	5,267.01	***

Chabot - Las Positas CCD Budget Status (Current Period) AS OF 30-SEP-2019

RUN DATE: 10/17/2019 TIME: 12:08 PM

PAGE: 13

\* \* \* REPORT CONTROL INFORMATION \* \* \*

PARAMETER SEQUENCE NUMBER: 78346

FISCAL YEAR: 20

CHART OF ACCOUNTS: 1 AS OF DATE: 30-SEP-2019

PRINT TOTALS: Y

PRINT NET TOTALS: Y

FROM FUND: 551%

TO FUND: 559999

FROM ORGN PRED: TO ORGN PRED:

FROM ORGN: TO ORGN:

ACCURAL INCLUDED: N

NUMBER OF PRINTED LINES PER PAGE: 55

RECORD COUNT: 26
